

University Sports Day Challenge

Presented by: Talah Alzuabi, Sara Alashar, Youssef Hashem, Taleen Alsobaie

Instructor: Dr. Sara Osailan



Key Metrics

- 12 Teams
- 8 Challenge Stations
- 7 Volunteers
- 2 Sessions
- 1 Successful Event

Project Overview

Scope

- Organized a university-wide wellness sports competition at Effat University
- Included separate sessions for girls (11:00–12:00) and boys (12:00–1:00)
- Planned and executed fully by the student project team
- Included registration, team formation, challenge stations, scoring, and prizes
- Focused on teamwork, fitness, student engagement, and healthy competition
- Managed within approved budget, schedule, and university regulations



Project Overview

Statement of Work (SOW)

Objective: Deliver a safe, engaging, and well-organized sports event for students.

Key Deliverables

- Approved project plan
- Student registration completed
- Stations prepared
- Volunteers managed
- Prizes distributed
- Final report submitted

Planning

- approvals
- schedule
- registration

Execution

- stations
- volunteers
- operations

Closeout

- scoring
- prizes
- report

Project Overview

UNIVERSITY SPORTS DAY CHALLENGE
WORK BREAKDOWN STRUCTURE (WBS)

1.0 PROJECT PLANNING AND APPROVAL

- 1.1 Define event concept and objectives
- 1.2 Determine event format (team competition)
- 1.3 Identify event date and time (11 AM – 1 PM)
- 1.4 Identify event location (Basketball Court)
- 1.5 Prepare project proposal and plan
- 1.6 Submit event request form
- 1.7 Coordinate with university departments (Dr. Pakenam, Dr. Tamer)
- 1.8 Confirm requirements and resources
- 1.9 Obtain official university approval

2.0 REGISTRATION AND TEAM MANAGEMENT

- 2.1 Create student registration form
- 2.2 Promote event and encourage registration
- 2.3 Form teams and confirm participants
- 2.4 Communicate event details and rules
- 2.5 Assign team numbers and prepare participant list
- 2.6 Prepare schedule (Girls 11–12 PM, Boys 12–1 PM)
- 2.7 Prepare scoring sheets and team tracking list

3.0 SPORTS ACTIVITIES AND EVENT DESIGN

- 3.1 Design challenge station system (6 stations)
- 3.2 Develop team competition format
- 3.3 Create scoring system (points for each station)
- 3.4 Plan sports challenges (basketball, table tennis, push-ups, planks, etc.)
- 3.5 Prepare station instructions and rules
- 3.6 Prepare equipment list for each station
- 3.7 Plan prize structure (1st, 2nd, 3rd place)

4.0 LOGISTICS, EQUIPMENT AND VOLUNTEER MANAGEMENT

- 4.1 Identify equipment requirements
- 4.2 Check and secure available equipment (Dr. Tamer)
- 4.3 Purchase or arrange missing materials
- 4.4 Recruit volunteers (approx. 7 volunteers)
- 4.5 Assign volunteers to stations
- 4.6 Train volunteers on rules, scoring, and safety
- 4.7 Prepare event layout and station setup plan
- 4.8 Prepare signage and station instructions
- 4.9 Prepare emergency and safety guidelines

5.0 EVENT EXECUTION AND CLOSURE

- 5.1 Set up all stations before event
- 5.2 Manage participant check-in and verification
- 5.3 Run Girls Session (11:00 AM – 12:00 PM)
- 5.4 Run Boys Session (12:00 PM – 1:00 PM)
- 5.5 Monitor activities and ensure safety
- 5.6 Calculate scores and validate results
- 5.7 Announce winners and distribute prizes
- 5.8 Collect feedback and evaluate event
- 5.9 Prepare final documentation and project report

Responsibility Assignment Matrix (RAM)

WBS Code	Task Description	Tala (Project	Youssef (Operation	Taleen (Sponsors	Sara (Marketing	Dr. Pakenam
1.1	Define event concept	A	S	N	S	N
1.5	Prepare project proposal	R	S	S	S	A
1.6	Submit event request form	R	N	N	N	A
1.9	Obtain official approval	R	N	N	N	A
2.1	Identify potential sponsors	A	N	R	S	N
2.4	Secure rewards / prizes	A	N	R	S	N
3.1	Design challenge stations	A	R	N	S	N
3.4	Plan sports games	A	R	N	S	N
4.1	Identify equipment	A	R	N	S	N
4.4	Recruit volunteers	A	N	N	R	N
4.6	Train volunteers	A	S	N	R	N
5.1	Set up activity stations	A	R	N	S	N
5.4	Monitor competitions	A	R	N	S	N
5.6	Distribute prizes	A	S	R	S	N
5.7	Collect feedback / evaluation	A	S	S	S	N
5.8	Prepare final report	R	N	N	N	A

Project Overview



Project Charter

Purpose

- Promote wellness and teamwork through a university sports event.

Scope

- Planning, execution, volunteers, prizes, reporting.

Budget

- SAR 1,200 + university resources.

Success Criteria

- On time, safe, engaged participants, within budget.


RISK ASSESSMENT

RISK IDENTIFICATION

- **The project team identified potential risks related to participation, equipment, volunteers, and event operations that could affect the success of the Sports Day Challenge.**

Risk Variable	Description of Risk	Potential Impact
Low Student Participation	Students may not register or attend the event because of class schedules, lack of interest, or other commitments.	This could reduce the success of the event, lower team competition, and make the event less engaging overall.
Participant Injury or Physical Exhaustion	The event includes physical activities such as push-ups, wall sit, burpees, plank, thrusters, couch flips, basketball, and running, which may cause fatigue or minor injuries.	Injuries or exhaustion may interrupt the event, reduce participation, and create safety concerns.
Equipment Shortage or Equipment Failure	Some sports equipment or station materials may be unavailable, damaged, or not prepared on time.	This may delay activities, reduce the number of functioning stations, or affect event quality.
Volunteer Shortage	The event requires volunteers/judges to manage stations, monitor rules, and support participants. If there are not enough volunteers, some stations may not operate properly.	Poor volunteer coverage may create disorganization, delays, and weak control during the event.
Poor Volunteer Coordination	Volunteers may not receive clear instructions or may not understand their assigned roles before the event begins.	This could lead to confusion at stations, poor participant guidance, and inconsistent event management.
Scoring Errors	Since some activities are based on repetition counts, timing, or performance quality, points may be counted incorrectly.	Incorrect scores may create fairness issues, participant complaints, and inaccurate final results.
Unclear Challenge Rules	Participants or volunteers may misunderstand the rules or scoring system for some challenge stations.	This may cause confusion, disputes, and slower event flow.
Team Imbalance	The event is based on 6 color-coded teams, but some teams may have stronger, more active, or more members than others.	This may make the competition unfair and reduce motivation for some participants.

Assessment of Probability & Consequences

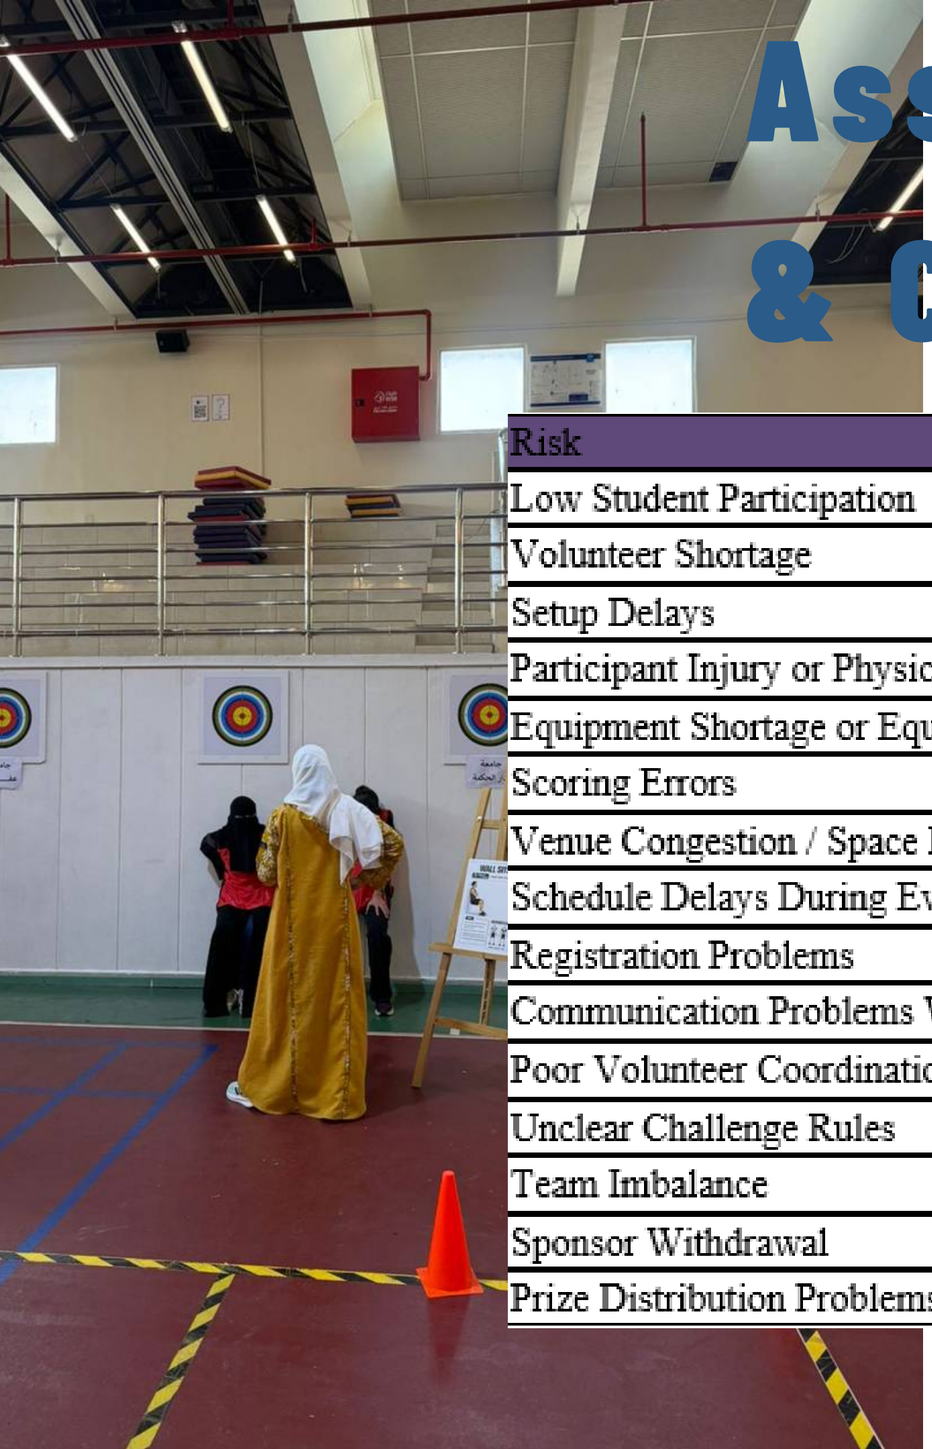

Risk	Probability	Impact	Risk Score	Priority
Low Student Participation	0.8	3	2.4	High
Volunteer Shortage	0.8	3	2.4	High
Setup Delays	0.8	3	2.4	High
Participant Injury or Physical Exhaustion	0.5	3	1.5	Medium
Equipment Shortage or Equipment Failure	0.5	3	1.5	Medium
Scoring Errors	0.5	3	1.5	Medium
Venue Congestion / Space Limitation	0.5	3	1.5	Medium
Schedule Delays During Event	0.5	3	1.5	Medium
Registration Problems	0.5	2	1.0	Medium
Communication Problems Within Team	0.5	2	1.0	Medium
Poor Volunteer Coordination	0.5	2	1.0	Medium
Unclear Challenge Rules	0.5	2	1.0	Medium
Team Imbalance	0.5	2	1.0	Medium
Sponsor Withdrawal	0.2	2	0.4	Low
Prize Distribution Problems	0.2	2	0.4	Low

A quantitative analysis was conducted by assigning numerical values to probability and impact. Risk scores were calculated to identify high-priority risks.


The highest risks identified were low participation, volunteer shortage, and setup delays.

Project SCHEDULE

Activity Network

Purpose of Activity Network


- Shows task sequence and dependencies
- Identifies critical path activities
- Highlights tasks that cannot be delayed
- Helps control total project duration

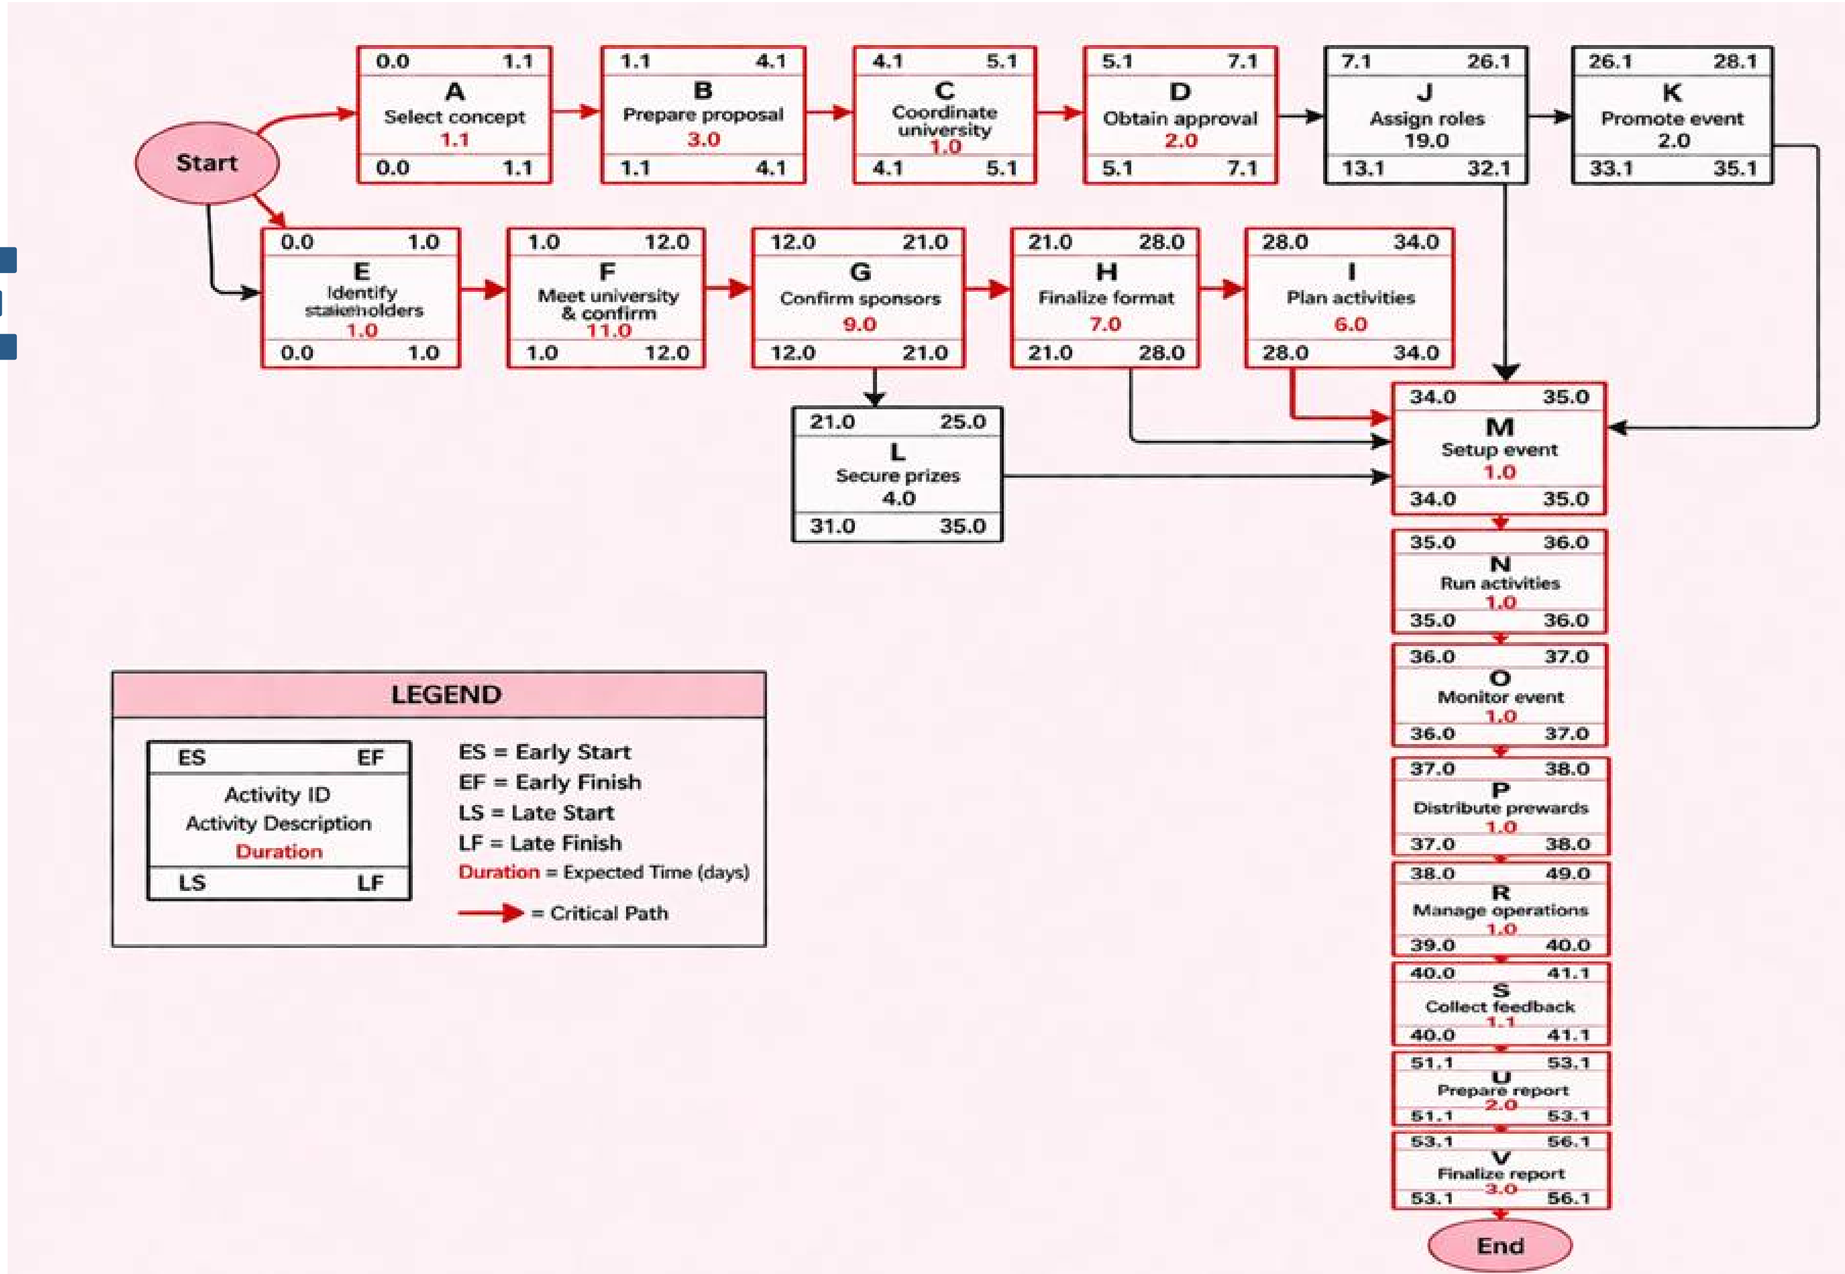

Gantt Chart

TASK ID	Task Description	Task Number	Predecessor	Resource	START DATE	WORK DAYS	END DATE	Critical Path
1.1.1	select topic	Task 01		Project Team	01-Apr-26	1	01-Apr-26	
1.1.2	prepare project proposal	Task 02	1	Project Team	02-Apr-26	3	06-Apr-26	YES
1.1.3	coordinate with university department	Task 03	2	Coordination Team	05-Apr-26	1	05-Apr-26	YES
1.1.4	obtain approval from administration (Milesto	Task 04	3	Management	06-Apr-26	2	07-Apr-26	YES
1.1.5	identify key stakeholders	Task 05	1	Project Team	01-Apr-26	1	01-Apr-26	
1.2.1	meet with university department	Task 06	4	Coordination Team	02-Apr-26	10	15-Apr-26	YES
1.2.2	confirm sponsors	Task 07	6	Marketing Team	12-Apr-26	8	21-Apr-26	
1.2.3	finalize event format and presentation	Task 08	7	Planning Team	15-Apr-26	4	20-Apr-26	YES
1.2.4	plan activities and games (Planning Compl	Task 09	8	Planning Team	17-Apr-26	2	20-Apr-26	YES
1.2.5	assign roles and responsibilities	Task 10	4	Project Team	06-Apr-26	12	21-Apr-26	YES
1.2.6	promote event (flyers/social media)	Task 11	10	Marketing Team	18-Apr-26	2	20-Apr-26	
1.2.7	prepare prizes and materials	Task 12	8	Logistics Team	15-Apr-26	3	17-Apr-26	
1.3.1	event execution (Event Day)	Task 13	12	Operations Team	20-Apr-26	1	20-Apr-26	YES
1.3.2	event execution (Event Day)	Task 14	13	Operations Team	20-Apr-26	1	20-Apr-26	YES
1.3.3	event execution (Event Day)	Task 15	14	Operations Team	20-Apr-26	1	20-Apr-26	YES
1.3.4	event execution (Event Day)	Task 16	15	Operations Team	20-Apr-26	1	20-Apr-26	YES
1.3.5	event execution (Event Day)	Task 17	16	Operations Team	20-Apr-26	1	20-Apr-26	YES
1.3.6	event execution (Event Day)	Task 18	17	Operations Team	20-Apr-26	1	20-Apr-26	YES
1.4.1	collect feedback	Task 19	18	Project Team	21-Apr-26	1	21-Apr-26	
1.4.2	analyze results	Task 20	19	Analysis Team	22-Apr-26	7	30-Apr-26	YES
1.4.3	prepare final report	Task 21	20	Project Manager	29-Apr-26	2	30-Apr-26	YES
1.4.4	finalize report	Task 22	21		01-May-26	3	05-May-26	

Gantt Chart

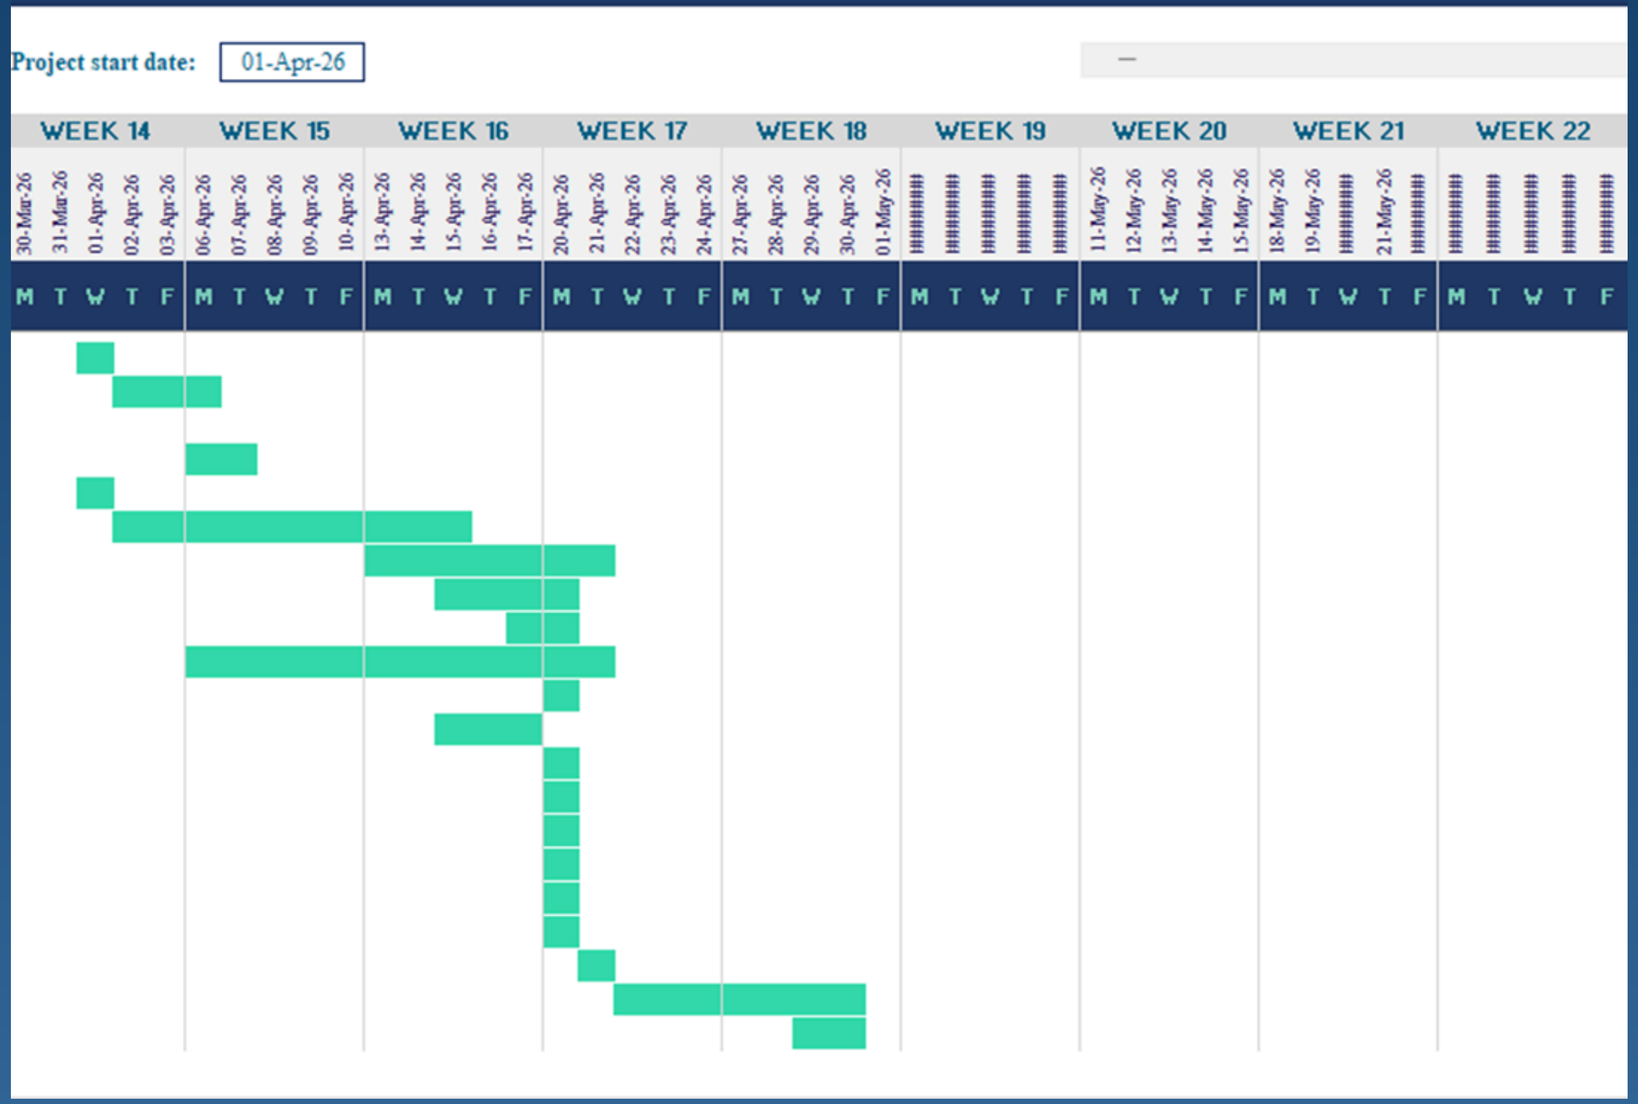

Schedule Planning Summary

- Project start date: 01-Apr-2026
- Total tasks planned: 22
- Responsibilities assigned to each team
- Critical activities marked in red

Execution Timeline

- Planning phase completed first
- Registration and promotion ran in parallel
- Event execution completed on schedule
- Final reporting completed after event day

Project Budget

Project Resources:

Human Resources

- 4 student project team members
- 24 volunteers
- University supervisors and faculty support

Physical Resources

- Basketball court venue
- Dumbbells, yoga mats, cones, timer
- Posters, shirts, score sheets

Support Resources

- University facilities provided free
- Volunteer labor support
- Administrative approvals



Project Budget

Cost Estimates:

Budget Breakdown

- Prizes & Rewards — SAR 800
- Printing & Promotion — SAR 100
- Team Setup Materials — SAR 80
- Supplies — SAR 70
- Contingency Reserve — SAR 150

Final Actual Cost: SAR 1,200

Project completed within budget

Stage	Estimate	Accuracy
Ballpark	SAR 950 – 1,650	±30%
Comparative	SAR 1,200	±15%
Feasibility	SAR 1,200	±10%
Definitive Final	SAR 1,200	±5%

Project Budget

Time-based Resources:

Week	Main Activity	Key Resources
Week 1	Planning & approvals	Project team
Week 2	Promotion & registration	Marketing team, volunteers
Week 3	Equipment & prize preparation	Operations team, sponsor lead
Week 4	Event execution	Full team + volunteers
Week 5	Evaluation & final report	Project manager, team

Peak resource usage occurred during event week when all members and volunteers were required.

Project Closeout

Close out accounts

- Final Budget: SAR 1,200
- Actual Cost: SAR 1,200
- Variance: 0 (on budget)
- No unpaid costs or debts
- All expenses matched planned categories

Challenges

- Low participation at the start
- Last-minute pressure
- Dependence on volunteers
- Minor delays between stations

Lesson Learned

- What went well:
- Strong teamwork & clear roles
- Stayed within budget
- High student engagement
- Smooth event execution
- Good use of university resources

Improvements for future

- Start promotion earlier
- Use digital registration system
- Add buffer time between stations

request form External Inbox

Pakenam Shiha, Ph.D 10:17 AM
to me, Ph.D

Good morning,
Your event has been approved. Please find the link to the QR code below.

If you prefer to use manual attendance, please use the attached Excel sheet. Make sure to enter the correct Student ID, as incorrect entries may result in the cancellation of points for that student.

Note the following when displaying the QR code:
1- You must sign in to the new Effat app to view the QR code.
2- The QR code will automatically become inactive at the end of the event, so please ensure all scans are completed beforehand.
3- Attendees must be signed into the new Effat app before scanning.
4- Students must be registered for the event in order to check in using the QR code.
5- This is a dynamic QR code and can only be displayed on a mobile device or iPad.
6- The QR code link can only be active on one device at a time.

https://mobileapp.effatuniversity.edu.sa/ajax_event_promote_email?uid=f9bfe1aeda74e67f8417ac3a3665910e&refresh=1

Use the attached sheet to add the organizers for the event as they receive double the hours.

Reply all Forward



33 EFFAT 2021
+966532293486, +966532446433, 7...

Sun, 19 Apr

All responses ar and will be used for academic purposes only.

Thank you for your participation! 🍵

https://forms.gle/DViEJ8yRGoC5hgWn8
8:16 PM

Taleen

Sports Day Sign Up
Don't miss out on April's exciting sports day! Bring your partner...
forms.gle

🚨 Sports Day is TOMORROW! 🔥

Get ready to compete, have fun, and win prizes! 🏆

⏰ Event Schedule:
- First hour: Girls only 🏋️
- Second hour: Guys only 🏋️

🥇 Top 3 winners from each group will win prizes!

⚡ Spots are VERY limited and people have already started registering —don't miss out!

👉 Sign up now before it's full!
https://forms.gle/cpAwJPseFDnkbzRc8
8:24 PM

1st Place winners!



Thank You
