Effat University

COLLEGE OF BUSINESS DEPARTMENT

Final Project

Spring 2026

University Sports Day Challenge
Spring 2026
OSCM 407

Instructor: Dr. Sara Osailan

Talah Alzuabi (S23108231)

Sara Alashar (S21207520)

Youssef Hashem (S22208109)

Taleen Alsobaie (S23108302)



Table of Contents

1. Project Overview 5

1.1 Purpose, Scope, Objectives, and Business Case 6

1.1.1 Scope 10

1.1.2 Statement of Work (SOW) 11

1.1.3 Business Case 12

1.2 Project Deliverables 14

1.3 Project Organization 17

1.4 Work Breakdown Structure (WBS) 22

1.4.1 Task Description Documentation 24

1.4.2 Organization Breakdown Structure (OBS) ... 26

1.5 Responsibility Assignment Matrix (RAM) 28

1.6 Work Authorization 29

1.7 Project Charter 33

2. Risk Assessment 35

2.1 Risk Identification 35

2.2 Assessment of Probability and Consequence (Qualitative) ... 37

2.3 Assessment of Probability and Consequence (Quantitative) ... 39

2.4 Mitigation Strategies 41

3. Project Schedule 43

3.1 Activity Duration Estimates 43

3.2 Gantt Chart 45

3.3 Activity Network 47

4. Project Budget 49

4.1 Project Resources 49

4.2 Other Costs 50

4.3 Cost Estimates 52

4.4 Time-Phased Budget 54

5. Project Close-out 56

5.1 Close Cost Accounts 56

5.2 Lessons Learned 57

1. Project Overview

1.1 Purpose, Scope, Objectives, and Business Case

Purpose

The purpose of the University Sports Day Challenge project is to plan, organize, and successfully execute a student-led sports and wellness event at Effat University that promotes physical activity, teamwork, healthy competition, and student engagement. Many university students spend long hours in classes and academic work, which can reduce physical movement and wellness habits. This project was designed to provide students with an enjoyable opportunity to participate in organized fitness challenges in an active campus environment.

The event was held during the official university activity time from 11:00 AM to 1:00 PM and was divided into two sessions. The girls' competition was conducted from 11:00 AM to 12:00 PM, while the boys' competition was conducted from 12:00 PM to 1:00 PM. This structure was used to improve organization, privacy, comfort, and participant flow.

The key deliverables of the project include planning the event, organizing teams, preparing challenge stations, coordinating volunteers, managing scoring operations, distributing prizes, promoting the event, and submitting the final project report.

Objectives

The main objectives of the project are:

Encourage students to participate in physical activity through a structured sports event.

Promote teamwork, motivation, and healthy competition among participants.

Increase student awareness of the importance of active lifestyles and wellness.

Successfully organize and manage a real campus event using project management principles.

Deliver the project within approved scope, budget, schedule, and quality expectations.

Measure project success through participation, execution quality, and feedback.

1.1.1 Scope

The scope of this project includes all planning, preparation, execution, and close-out activities related to the University Sports Day Challenge held at Effat University.

Problem Statement: Many university students experience limited physical activity due to academic workload, long lecture hours, and sedentary routines. This can negatively affect health, energy levels, motivation, and student well-being. There is a need for an engaging and accessible campus activity that encourages movement, teamwork, and healthy habits in a fun environment.

Requirements Gathering: To identify project requirements, the team consulted several stakeholders during the planning stage:

- Weeks 1–2: Discussions were held among project team members to define the event concept, possible formats, and required resources.
- Weeks 2–3: Students were consulted informally to understand preferred sports activities, team interest, and suitable timing.
- Weeks 3–4: Dr. Pakenam Shiha was consulted regarding official approval procedures, activity scheduling, and university event requirements.
- Weeks 4–5: Dr. Tamer was consulted regarding court availability, sports equipment, and activity feasibility.
- Weeks 5–6: Internal team meetings were held to confirm final layout, volunteer needs, scoring system, and prize structure.

Information Gathering: Based on the investigation, the following critical features were identified:

- Activities should be short, competitive, and easy to understand.
- Multiple stations are needed to reduce waiting time and improve flow.
- Team competition increases motivation and engagement.
- Volunteers are required for scoring, timing, and participant guidance.
- Clear written instructions should be displayed at each station.
- Prizes increase participation interest.
- The basketball court is the most suitable venue for layout and movement.
- Gender-separated sessions improve comfort and organization.

Project Constraints:

- Limited student budget for prizes and materials.
- Limited preparation time during the semester.
- Dependence on university approvals before execution.
- Availability of sports facilities and equipment.
- Need for sufficient volunteers on event day.
- Fixed activity time from 11:00 AM to 1:00 PM.

Alternatives Analysis

Several event alternatives were considered:

- Traditional Sports Tournament
  Rejected because it requires more time, referees, and longer scheduling.
- Wellness Seminar / Awareness Event
  Rejected because it offers lower physical engagement and less participation energy.

- University Sports Day Challenge (Selected Option)
  Selected because it allows many students to participate quickly, creates excitement, requires moderate resources, and supports health and teamwork goals.

Business Case Documentation

The University Sports Day Challenge creates value for multiple stakeholders.

- Students: Improve physical activity, enjoyment, teamwork, and campus engagement.
- University: Supports wellness initiatives, student life, and positive campus culture.
- Project Team: Gains practical experience in planning, budgeting, coordination, leadership, and event management.
- Volunteers: Gain involvement experience and teamwork skills.

The project demonstrates that a low-cost student-led initiative can create meaningful campus impact when managed effectively.

1.1.2 Statement of Work (SOW)

The University Sports Day Challenge was executed through a structured project lifecycle consisting of planning, preparation, execution, and close-out phases.

1. Key Milestones:

- Project concept selected and team roles assigned.
- University approvals obtained.
- Student registration form distributed.
- Teams finalized and volunteers assigned.
- Event layout and challenge stations prepared.
- Prizes purchased and materials printed.
- Event successfully executed.
- Winners announced and prizes distributed.
- Final report completed and submitted.

2. Resource Requirements

- Basketball court venue.
- Dumbbells, yoga mats, cones, timer, sports tools.
- Posters and challenge instruction signs.
- Registration forms and scoring sheets.
- Four project team members.
- Approximately seven volunteers / station judges.
- Budget for prizes and printing.

- Administrative support and approvals.

3. Risks and Concerns

- Low student participation.
- Equipment shortage or failure.
- Volunteer shortage or poor coordination.
- Scoring errors or disputes.
- Setup delays.
- Participant fatigue or minor injury.
- Time overruns during event execution.
- Sponsor support not secured.

4. Acceptance Criteria

- The project will be considered successful if:
- Planned teams participate successfully.
- Event starts and finishes within approved schedule.
- All challenge stations operate effectively.
- Scores are recorded fairly and accurately.
- Winners receive prizes successfully.
- Participants show positive engagement.
- Final report is submitted on time.

1.3 Project Organization

The University Sports Day Challenge was managed through a functional student project team structure supported by university stakeholders. The project team consisted of four members, with each member assigned responsibility for a major operational area. This structure was selected to ensure clear authority, effective communication, task specialization, and successful event execution within limited time and resources.

The project operated under the supervision of university representatives who provided approvals, facilities support, and administrative guidance. Functional managers were responsible for specialized work areas, while the Project Manager maintained overall coordination, schedule control, and final accountability.

1.3.1 Project Organization Type

The project followed a Functional Matrix Structure.

Under this structure:

- The Project Manager had overall authority for planning, coordination, scheduling, and monitoring progress.
- Functional team members managed their assigned specialty areas such as operations, sponsorship, and marketing.
- Major approvals required support from university supervisors and sponsors.
- Some responsibilities were shared jointly between the Project Manager and functional leads.

This structure was appropriate because the project required coordination across several small work areas while maintaining centralized leadership.

1.3.2 Executive Sponsors and University Support

Project Sponsor

Effat University Administration

Responsibilities:

- Provide final approval for the Sports Day Challenge event.
- Ensure project compliance with university rules and policies.
- Support use of university facilities and activity time.
- Review major project decisions when required.

University Supervisor

Dr. Pakenam Shiha

Responsibilities:

- Approve official event request and execution permission.
- Coordinate with university departments.
- Support venue allocation and event timing.
- Provide administrative guidance throughout the project.

Sports Activities Support

Dr. Tamer

Responsibilities:

- Support use of sports court and available equipment.
- Advise on event layout and challenge feasibility.
- Assist with operational readiness of sports facilities.

PR / External Communication Support

Ms. Maha – PR Department

Responsibilities:

- Support external communication when required.
- Review sponsorship or promotional requests if needed.
- Provide communication guidance for outreach activities.

1.3.3 Student Project Management Team

Project Manager

Talah Alzuabi

Responsibilities:

- Overall leadership of the project.
- Develop project schedule and monitor deadlines.
- Coordinate all team members and stakeholders.
- Approve task assignments and monitor progress.
- Ensure successful execution of the event.
- Prepare final reporting and closeout activities.

Operations Manager

Youssef Hashem

Responsibilities:

- Manage event logistics and operational planning.
- Organize basketball court layout and station flow.
- Supervise setup of activity stations and equipment.
- Coordinate event-day operations and execution support.

Joint Responsibility with Project Manager:

- Final event setup approval.
- Event-day schedule control.
- Operational issue resolution.

Sponsorship and Partnerships Manager

Taleen Alsobaie

Responsibilities:

- Identify potential sponsors or prize contributors.
- Coordinate reward sourcing and participant prizes.
- Manage partnership communication efforts.
- Support procurement of materials if needed.

Joint Responsibility with Project Manager:

- Sponsor decisions.
- Budget alignment for rewards.
- Final prize approvals.

Marketing and Volunteer Manager

Sara Alashar

Responsibilities:

- Promote the event to university students.
- Manage registration communication.
- Recruit volunteers and assign duties.
- Coordinate volunteer briefing and supervision.
- Support participant check-in process.

Joint Responsibility with Project Manager:

- Participant turnout targets.
- Registration control.
- Volunteer staffing adequacy.

1.3.4 Volunteers

Approximately seven volunteers were assigned during execution to support station operations and participant management.

Responsibilities:

- Monitor challenge stations.
- Count repetitions or timing results.
- Record team scores.
- Guide participants between stations.
- Support safety and event flow.

Assist in prize distribution when needed.

1.3.5 Project Reporting Structure


University Administration (Project Sponsor)

|

Dr. Pakenam

(University Supervisor)

|

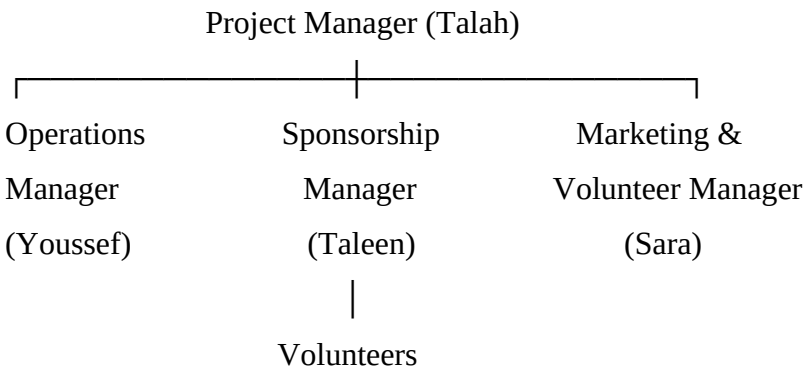

1.3.6 Communication and Authority Flow

- Functional managers reported progress to the Project Manager.
- The Project Manager communicated major updates to university supervisors.
- University approvals were required for significant changes involving venue, schedule, or policy.
- Daily team coordination was managed internally through meetings and messaging channels.

1.3.7 Project Stakeholder Sign-Off


Stakeholder	Role	Signature	Date
Effat University Administration	Project Sponsor	_____	_____
Dr. Pakenam Shiha	University Supervisor	_____	_____
Dr. Tamer	Sports Support	_____	_____
Ms. Maha	PR Support	_____	_____

1.4 Work Breakdown Structure (WBS)

The Work Breakdown Structure (WBS) for the University Sports Day Challenge was developed to divide the project into manageable deliverables and work packages. The WBS organizes the project into major phases including planning, sponsorship, event design, logistics, and execution. This structure improves task control, responsibility assignment, scheduling, budgeting, and performance monitoring throughout the project lifecycle.

The WBS below includes all key deliverables and supporting work packages required to successfully complete the project.

1.4.1 WBS Hierarchical Structure

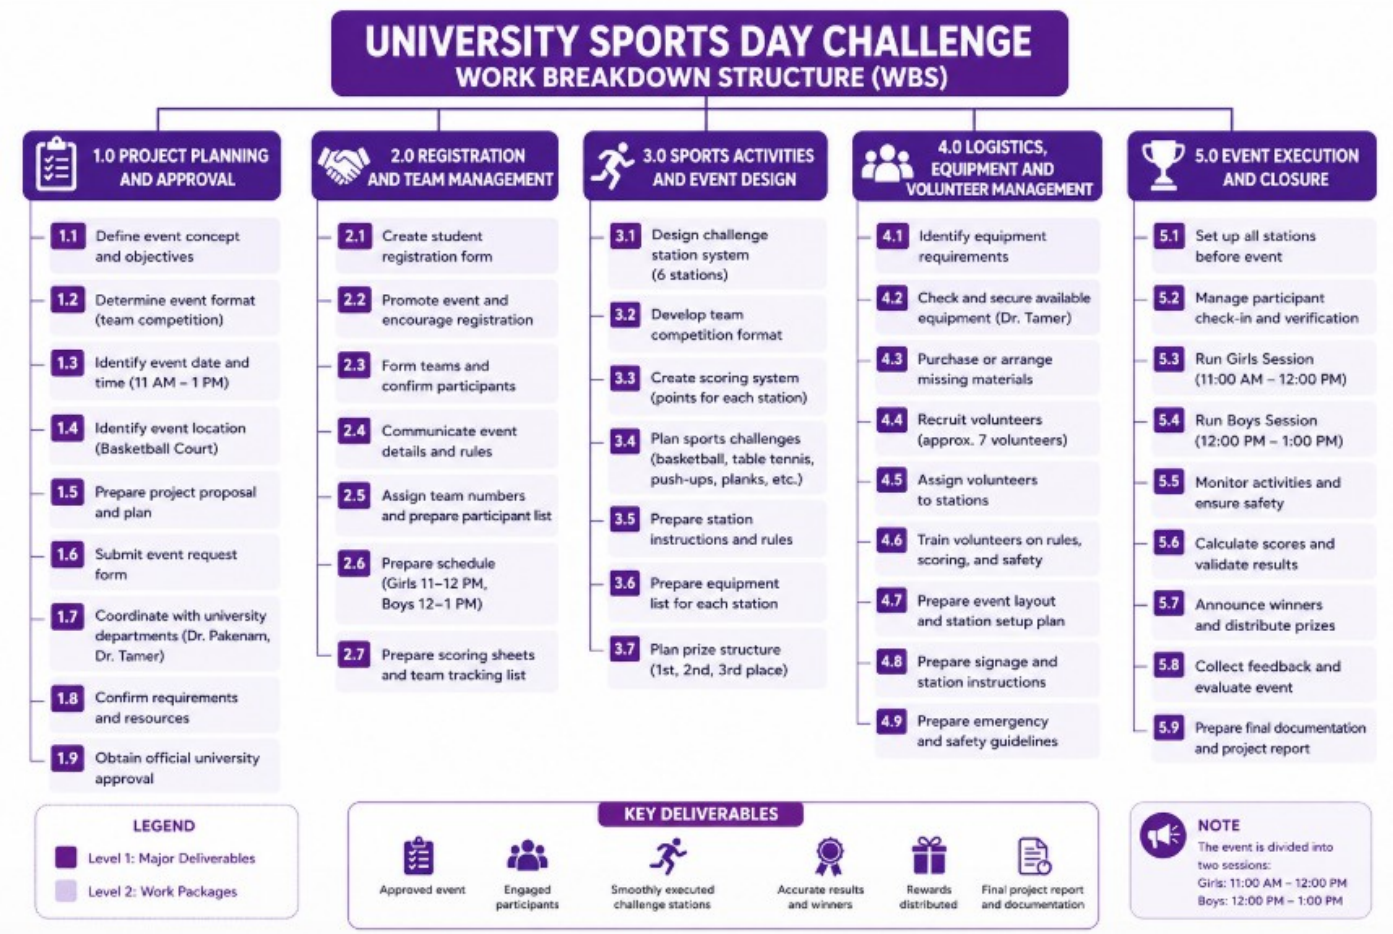

1.4.2 WBS Stakeholder Approval

Stakeholder	Role	Approval
Effat University Administration	Project Sponsor	Approved
Dr. Pakenam Shiha	University Supervisor	Approved
Dr. Tamer	Sports Support	Approved

1.4.3 Project Task Description Documentation

Task Data Sheet 1

Task ID: 1.6

Task Name: Submit event request form and obtain approval

Objective: To secure official university approval required to conduct the University Sports Day Challenge on campus.

Description / Activities:

- Prepare the official event request form.

- Attach required project details including date, time, venue, and objectives.
- Submit request to the responsible university department.
- Follow up with stakeholders until final approval is granted.

Responsible Person: Project Manager (Talah Alzuabi)

Start Date: Week 3, 2026

End Date: Week 4, 2026

Deliverables / Output:

- Completed event request form.
- Approved authorization to conduct the event.
- Confirmed activity time and venue access.

Resources Required: Project proposal, approval form, communication channels, university contacts.

Acceptance Criteria:

- Form is submitted correctly and on time.
- Approval is officially granted.
- Basketball court and activity slot are confirmed.

Task Data Sheet 2

Task ID: 1.2.6

Task Name: Promote event and student registration

Objective: To generate student interest and awareness for the University Sports Day Challenge and encourage registration from participants.

Description / Activities:

- Design promotional posters and digital announcements.
- Share event details through WhatsApp groups and university channels.
- Encourage students to register through the online form.
- Explain event concept, timing, prizes, and team competition format.

Responsible Person: Marketing & Volunteer Manager (Sara Alashar)

Start Date: Week 8, 2026

End Date: Week 10, 2026

Deliverables / Output:

- Printed posters and digital promotional materials.
- Student registration form distributed.
- Participant list and team sign-ups completed.

Resources Required: Canva/design tools, printer, paper, digital platforms, registration form, volunteers.

Acceptance Criteria:

- Promotional materials are approved by the Project Manager.
- Materials are distributed before the event date.
- Target number of students successfully register.

Task Data Sheet 3

Task ID: 1.3.1

Task Name: Implement all planned event activities on campus

Objective: To successfully execute the University Sports Day Challenge according to the approved plan, schedule, and competition format.

Description / Activities:

- Set up all challenge stations on the basketball court.
- Manage participant check-in and team organization.
- Conduct all physical challenges according to rules.
- Monitor scoring, timing, and participant flow.
- Announce winners and distribute prizes.

Responsible Person: Operations Manager (Youssef Hashem)

Start Date: Event Day

End Date: Event Day

Deliverables / Output:

- Successfully completed sports challenge event.
- Fully operational challenge stations.
- Recorded scores and final winners announced.
- Prizes distributed to winning teams.

Resources Required: Basketball court, sports equipment, mats, dumbbells, cones, timer, score sheets, volunteers, prizes.

Acceptance Criteria:

- Event is executed according to planned schedule.
- All stations operate safely and effectively.
- Scores are recorded fairly and accurately.
- Minimum planned number of teams participate successfully.

1.4.4 Organization Breakdown Structure (OBS)

Department / Role	Main Responsibility
University Administration	Final approvals and institutional support

Dr. Pakenam Shiha	Event supervision and coordination
Dr. Tamer	Sports facilities and equipment support
PR / External Support	Communication and sponsorship guidance
Project Manager	Overall planning and control
Operations Manager	Logistics, setup, venue flow
Sponsorship Manager	Rewards, sponsors, procurement
Marketing & Volunteer Manager	Promotion, registration, volunteers
Volunteers	Station management and scoring

1.4.5 Cost Accounts Across Cooperating Departments

Role	Planning	Sponsorship	Logistics
Project Manager	Cost Account		
Sponsorship Manager		Cost Account	
Operations Manager			Cost Account
Marketing Manager	Cost Account		

1.5 Responsibility Assignment Matrix (RAM)

R = Responsible

A = Accountable / Approval

S = Support

N = Notified

WBS Code	Task	Tala (PM)	Youssef (Ops)	Taleen (Sponsor)	Sara (Mktg/Vol.)	Dr. Pakenam
1.1	Define event concept	A/R	S	N	S	N
1.5	Prepare event	A/R	S	S	S	N

	proposal					
1.6	Submit event request form	R	N	N	N	A
1.9	Obtain official approval	R	N	N	N	A
2.1	Identify potential sponsors	A	N	R	S	N
2.4	Secure rewards / prizes	A	N	R	S	N
3.1	Design challenge stations	A	R	N	S	N
3.4	Plan sports games	A	R	N	S	N
4.1	Identify equipment requirements	A	R	N	S	N
4.4	Recruit volunteers	A	N	N	R	N
4.6	Train volunteers	A	S	N	R	N
5.1	Set up activity stations	A	R	N	S	N
5.4	Monitor competitions	A	R	N	S	N
5.6	Distribute prizes	A	S	R	S	N

5.7	Event evaluation	A/R	S	S	S	N

1.6 Work Authorization

The Work Authorization section defines the formal approval process, authority levels, contract terms, conditions, notifications, and corrective actions required to control work activities during the University Sports Day Challenge project. Its purpose is to ensure that project tasks are performed only after proper authorization, responsibilities are clearly assigned, and changes are managed in an organized manner. Because this project involved university facilities, student participants, scheduling constraints, and limited resources, controlled authorization was necessary to avoid delays, confusion, misuse of resources, or unauthorized commitments.

1.6.1 Work Authorization Plan

No major project activity could begin without prior approval from the authorized project leadership.

Authorized Approvers

Activity Type	Approving Authority
Internal planning tasks	Project Manager
Budget spending / prize purchases	Project Manager
Volunteer assignments	Project Manager
Event venue usage	University Administration / Dr. Pakenam
Schedule changes affecting event date/time	University Supervisor
Equipment borrowing from university	Dr. Tamer / University Support
External sponsorship commitments	Project Manager with University awareness

1.6.2 Authorization Process

1. The responsible team member submits the task request or activity need to the Project Manager.
2. The Project Manager reviews scope, timing, manpower, and required resources.
3. If university approval is needed, the request is escalated to Dr. Pakenam or the relevant department.
4. Once approved, the task is assigned to the responsible member.
5. Work begins only after approval is confirmed.
6. Task completion is reported back to the Project Manager for closeout and status tracking.

1.6.3 Contract Terms and Conditions

Although the project was a university student event and not a commercial project, certain working agreements applied with supporting parties, volunteers, and any sponsor contributors.

General Terms

- All participants and helpers must follow university rules and safety procedures.
- Equipment must be used responsibly and returned in original condition.
- Promotional activities require prior approval if using university branding.
- Prize commitments must be confirmed before public announcement.
- Volunteers must attend assigned shifts on event day.
- Sponsors providing rewards must deliver items before the event date.
- No unauthorized financial commitments may be made by team members.

1.6.4 Penalty Clauses and Trigger Events

The project used administrative corrective actions rather than legal penalties.

Trigger Event	Corrective Action / Penalty
Team member misses deadline without notice	Task reassigned and warning issued
Failure to attend mandatory meeting	Responsibility review by Project Manager
Volunteer absence on event day	Immediate replacement assignment
Late prize delivery by sponsor	Sponsor recognition removed or substituted rewards arranged
Damage to borrowed equipment due to negligence	Responsible party reported and replacement coordination required
Unauthorized spending	Expense not reimbursed without approval
Failure to communicate delay or issue	Escalation to Project Manager

1.6.5 Notification Requirements

All relevant stakeholders were required to be informed of significant project changes, approvals, delays, or risk events.

Official Communication Channels

- WhatsApp project group
- Email communication
- In-person meetings
- Direct calls for urgent matters

Stakeholders to be Notified

Change / Issue	Stakeholders to Notify
Event date or time change	All team members, volunteers, Dr. Pakenam
Venue change	Team members, volunteers, university supervisor
Budget issue	Project Manager, Sponsorship Lead
Volunteer shortage	Project Manager, Sara
Equipment issue	Project Manager, Youssef, Dr. Tamer
Sponsor cancellation	Project Manager, Taleen
Major schedule delay	Entire project team

1.6.6 Escalation Procedure

If an issue could not be solved by the responsible member:

1. Report immediately to the Project Manager.
2. Functional lead attempts resolution.
3. If university support is needed, escalate to Dr. Pakenam or relevant department.
4. Final decision communicated to all impacted members.

1.6.7 Work Authorization Approval

Stakeholder	Role	Approval
Talah Alzuabi	Project Manager	Approved
Dr. Pakenam Shiha	University Supervisor	Approved
Effat University Administration	Project Sponsor	Approved

1.6.8 Summary

This Work Authorization system ensured that tasks were properly approved, responsibilities were controlled, resources were protected, and project execution remained aligned with schedule and university requirements.

1.7 Project Charter

1.7.1 Project Purpose and Justification

The objective of this project is to organize the University Sports Day Challenge at Effat University as a student-led wellness event designed to encourage physical activity, teamwork, and healthy competition among students. The project aims to create an enjoyable environment where students participate in organized sports challenges while increasing awareness of the importance of maintaining an active lifestyle.

One of the main reasons this project is proposed is the growing need to reduce sedentary habits among university students caused by long study hours and academic pressure. The event also provides an opportunity for students to apply project management principles in a real setting, improve teamwork and leadership skills, and contribute positively to campus life and student well-being.

1.7.2 Project Objectives

Organize and successfully execute a campus sports challenge event for Effat University students.
Encourage students to participate in physical activities through engaging challenge stations.
Promote teamwork, motivation, and healthy competition among participants.
Apply project management principles such as planning, scheduling, coordination, communication, and control.
Measure project success through participation levels, smooth execution, and participant feedback.

1.7.3 Project Scope Summary

The project includes planning, organizing, and executing the University Sports Day Challenge on campus at Effat University. Activities include student registration, team formation, challenge station preparation, event promotion, volunteer coordination, scoring management, prize distribution, and post-event evaluation. Activities excluded from the project include long-term fitness programs, off-campus sports events, recurring tournaments, or major external commercial sponsorship programs.

1.7.4 Key Stakeholders

Stakeholder	Role / Responsibility
Dr. Sara Osailan	Course Instructor, Academic Supervisor
Dr. Pakenam Shiha	Dean of Student Affairs, Project Sponsor
Dr. Tamer	Sports Supervisor and Facility Support
Project Team Members	Planning, coordination, execution, reporting
Volunteers	Station supervision, score tracking, participant support
Effat University Students	Event participants and target audience

1.7.5 Project Authority and Responsibility

The project will be executed under the supervision of the Course Instructor, who holds academic authority for review and evaluation. The Dean of Student Affairs provides formal institutional approval for conducting the event.
The Project Manager holds operational authority and is responsible for coordinating daily tasks, assigning responsibilities, monitoring progress, and ensuring project completion. Team members are responsible for

completing assigned duties in planning and execution. Major decisions regarding facilities, scheduling, and event approvals must receive university authorization before implementation.

1.7.6 Constraints and Assumptions

Constraints:

- The project must be completed within the academic semester timeline.
- Budget is limited and relies mainly on student contributions and available university resources.
- Event timing must fit within the approved university activity hours.
- Venue and equipment availability depend on university scheduling.
- Approval is required before execution of event activities.

Assumptions:

- Team members will contribute actively to assigned responsibilities.
- Students will show interest in participating due to promotion and prizes.
- University equipment and facilities will be available on event day.
- Volunteers will attend and support station operations.
- Weather and operational conditions will not prevent the event from proceeding.

1.7.7 Success Criteria

- At least the planned number of teams successfully participate.
- The event is completed during the approved time period.
- All challenge stations operate effectively.
- Scores are recorded accurately and winners are announced fairly.
- Participants show positive engagement and feedback.
- Final report and presentation are submitted successfully.

1.7.8 Authorization and Sign-Off

This Project Charter formally authorizes the University Sports Day Challenge and grants permission to use approved university resources necessary for planning and execution.

Name	Position	Signature	Date
Dr. Pakenam Shiha	Project Sponsor	_____	_____
Dr. Sara Osailan	Course Instructor	_____	_____
Talah Alzuabi	Project Manager	_____	_____
Project Team Members	Execution Team	_____	_____

2. Risk Management

2.1 Risk Identification

Risk Identification

Organizing the **Sports Day Challenge Event** involves coordination between participants, volunteers, sponsors, equipment, and university arrangements. Based on the project plan and updated meeting notes, several risks were identified that may affect the event's execution and overall success. The table below outlines the main project risks, their description, and their potential impact on the event.

Risk Variable	Description of Risk	Potential Impact
Low Student Participation	Students may not register or attend the event because of class schedules, lack of interest, or other commitments.	This could reduce the success of the event, lower team competition, and make the event less engaging overall.
Participant Injury or Physical Exhaustion	The event includes physical activities such as push-ups, wall sit, burpees, plank, thrusters, couch flips, basketball, and running, which may cause fatigue or minor injuries.	Injuries or exhaustion may interrupt the event, reduce participation, and create safety concerns.
Equipment Shortage or Equipment Failure	Some sports equipment or station materials may be unavailable, damaged, or not prepared on time.	This may delay activities, reduce the number of functioning stations, or affect event quality.
Volunteer Shortage	The event requires volunteers/judges to manage stations, monitor rules, and support participants. If there are not enough volunteers, some stations may not operate properly.	Poor volunteer coverage may create disorganization, delays, and weak control during the event.
Poor Volunteer Coordination	Volunteers may not receive clear instructions or may not understand their assigned roles before the event begins.	This could lead to confusion at stations, poor participant guidance, and inconsistent event management.
Scoring Errors	Since some activities are based on repetition counts, timing, or performance quality, points may be counted incorrectly.	Incorrect scores may create fairness issues, participant complaints, and inaccurate final results.
Unclear Challenge Rules	Participants or volunteers may misunderstand the rules or scoring system for some challenge stations.	This may cause confusion, disputes, and slower event flow.
Team Imbalance	The event is based on 6 color-coded teams, but some teams may have stronger, more active, or	This may make the competition unfair and reduce motivation for

	more members than others.	some participants.
Registration or Participant Form Issues	Some students may not complete the registration form properly, or there may be confusion during participant check-in.	This may cause delays, team assignment issues, and difficulty organizing participants efficiently.
Setup Delays	Event setup such as station preparation, registration desk setup, team organization, and prize arrangement may take longer than expected.	A delayed setup may cause the event to start late and affect the planned schedule.
Sponsor Withdrawal or Lack of Sponsor Support	Sponsors such as gyms, food brands, or other businesses may cancel or fail to provide promised support.	This may affect prizes, giveaways, sponsorship value, and the attractiveness of the event.
Prize Shortage or Distribution Problems	Prizes may not be enough, may arrive late, or may not be distributed properly to winners.	This may reduce participant satisfaction and create complaints at the end of the event.
Venue or Space Limitations	The event space may become crowded due to challenge stations, teams, volunteers, and sponsor booths being in one area.	Limited space may affect movement, safety, and the smooth flow of the event.
Schedule Delays During the Event	One or more stations may take longer than expected, causing timing issues across the event.	Delays may affect the full event schedule and reduce the number of completed activities.
Communication Problems Within the Team	Miscommunication between team members may affect planning, setup, volunteer management, sponsorship, or event-day coordination.	This may lead to mistakes, delays, and weaker overall event execution.

2.2 ASSESSMENT OF PROBABILITY AND CONSEQUENCE (QUALITATIVE)

The table below presents a qualitative assessment of the main risks associated with the University Sports Day Challenge. Each risk was evaluated based on two factors: likelihood (the chance of occurrence) and consequence (the impact on the project).

Risks were rated as Low (L), Medium (M), or High (H). A low likelihood means the risk is unlikely to occur, medium means it may occur, and high means it is likely to occur. Likewise, a low consequence

indicates minor disruption, medium indicates noticeable disruption, and high indicates serious disruption that may significantly affect the event's success, safety, or participant experience.

The ratings were determined through team discussion based on the project scope, event logistics, volunteer and sponsor dependency, equipment requirements, and participant safety considerations. The assessment was also reviewed by the project's key stakeholders to ensure the ratings reflect realistic event conditions and operational expectations.

Qualitative Risk Assessment Table

Risk	Probability (Likelihood)	Consequence (Impact)	Risk Rating	Explanation / Remarks
Low Student Participation	High	High	High	The event depends heavily on student turnout. Low participation would directly reduce engagement,
Participant Injury or Physical Exhaustion	Medium	High	High	Physical activities may lead to fatigue or minor injuries, affecting
Equipment Shortage or Equipment Failure	Medium	High	High	Missing or damaged sports equipment may prevent some challenge stations from operating properly.
Volunteer Shortage	Medium	High	High	Insufficient volunteers would reduce control over stations, registration, and participant flow.
Scoring Errors	Medium	High	High	Incorrect counting or timing may create fairness issues and participant complaints.
Registration or Participant Form Issues	Medium	Medium	Medium	Registration errors may create delays, check-in confusion, or incorrect team assignments.
Setup Delays	Medium	High	High	Delays in station setup, registration, or equipment arrangement may affect the start time and schedule.
Sponsor Withdrawal or Lack of Sponsor Support	Low	High	Medium	Sponsor cancellation would affect prizes, giveaways, and the attractiveness of the event.
Communication	Medium	Medium	Medium	Miscommunication may affect

Risk	Probability (Likelihood)	Consequence (Impact)	Risk Rating	Explanation / Remarks
Problems Within the Team				planning, coordination, and event-day execution.

Evidence of Assessment and Stakeholder Signoff

The qualitative risk assessment was developed through team discussion and stakeholder consultation. The ratings were based on the project scope, expected event-day challenges, operational requirements, and previous planning discussions. The following stakeholders reviewed or contributed to the assessment based on their project responsibilities:

Stakeholder	Role	Approval / Signoff
University Administration	Project Sponsor	Approved
Dr. Pakenam	University Supervisor	Approved
Ms. Maha	PR Department	Approved
Talah	Project Manager	Approved
Youssef	Operations Manager	Approved
Taleen	Sponsorship Manager	Approved
Sara	Marketing & Volunteer Manager	Approved

2.3 ASSESSMENT OF PROBABILITY AND CONSEQUENCE (QUANTITATIVE)

In addition to the qualitative assessment, a quantitative analysis is conducted to assign numerical values to both the probability and impact of each identified risk. This allows for a more precise evaluation and prioritization of risks.

Criteria for Assessment

To ensure consistency, the following scales are used:

Probability (Likelihood):

• Low = 0.2

• Medium = 0.5

• High = 0.8

Impact (Consequence):

• Low = 1

• Medium = 2

• High = 3

The Risk Score is calculated using the formula:

• **Risk Score = Probability × Impact**

Risk scores above 2.0 are considered high priority, scores between 0.5 and 2.0 are classified as medium priority, and scores below 0.5 are considered low priority.

Quantitative Risk Analysis Table

Risk	Probability	Impact	Risk Score	Priority
Low Student Participation	0.8	3	2.4	High
Volunteer Shortage	0.8	3	2.4	High
Setup Delays	0.8	3	2.4	High
Participant Injury or Physical Exhaustion	0.5	3	1.5	Medium
Equipment Shortage or Equipment Failure	0.5	3	1.5	Medium
Scoring Errors	0.5	3	1.5	Medium
Venue Congestion / Space Limitation	0.5	3	1.5	Medium
Schedule Delays During Event	0.5	3	1.5	Medium
Registration Problems	0.5	2	1.0	Medium
Communication Problems Within Team	0.5	2	1.0	Medium
Poor Volunteer Coordination	0.5	2	1.0	Medium
Unclear Challenge Rules	0.5	2	1.0	Medium
Team Imbalance	0.5	2	1.0	Medium
Sponsor Withdrawal	0.2	2	0.4	Low
Prize Distribution Problems	0.2	2	0.4	Low

2.3.1 Risk Justification

The quantitative analysis shows that the most critical risks are Low Student Participation, Volunteer Shortage, and Setup Delays, all having the highest risk scores (2.4). These risks require immediate attention because they can directly affect the success, organization, and smooth execution of the Sports Day Challenge.

Risks such as participant injury, equipment shortage, scoring errors, venue congestion, and schedule delays fall into the medium category. While they are less critical, they still require monitoring, preparation, and control measures during the event.

Low-risk factors, including sponsor withdrawal and prize distribution problems, have minimal impact but should still be acknowledged to ensure overall readiness.

2.4 Mitigation Strategies

RISK	STRATEGY	MITIGATION ACTIONS	EXPLANATION / REMARKS
Low Student Participation	Minimize	Promote event through social media, emails, and campus announcements. Collaborate with student clubs. Offer prizes and incentives. Allow easy/on-site registration.	Increasing awareness and incentives will improve turnout and engagement, reducing the likelihood of low participation.
Participant Injury or Physical Exhaustion	Minimize	Provide safety instructions. Assign trained supervisors. Ensure first aid availability. Adjust activity difficulty levels.	Safety measures reduce the risk of injuries and ensure participants can complete activities safely.
Equipment Shortage or Equipment Failure	Minimize / Transfer	Prepare backup equipment. Test equipment before the event. Assign technical support team. Rent from reliable suppliers.	Backup plans and reliable sources reduce disruptions and ensure all stations function properly.

Volunteer Shortage	Minimize	Recruit extra volunteers. Offer incentives (certificates/hours). Assign clear roles and schedules.	Having backup volunteers ensures smooth operation and avoids delays or unmanaged stations.
Scoring Errors	Minimize	Use simple scoring system. Train volunteers. Assign score verification role. Use tracking sheets or digital tools.	Clear systems and verification reduce errors and ensure fairness in results.
Registration or Participant Form Issues	Minimize	Use simple registration system. Double-check data. Provide help desk for issues.	Proper organization reduces confusion, delays, and incorrect participant assignments.
Setup Delays	Minimize	Create checklist and schedule. Start setup early. Assign teams. Conduct pre-event walkthrough.	Good preparation ensures the event starts on time and runs smoothly.
Sponsor Withdrawal or Lack of Sponsor	Transfer / Accept	Confirm sponsors early. Prepare backup sponsors. Adjust	Backup planning reduces impact on event quality if

Support		prizes if needed.	sponsors withdraw.
Communication Problems Within the Team	Minimize	Use clear communication channels. Assign team leaders. Hold meetings. Share final plan.	Strong communication ensures coordination and reduces mistakes or delays.

3. Project Schedule

3.1 Activity Duration Estimates (PERT)

Use this exactly:

Activity duration estimates for the **University Sports Day Challenge** were developed using the Program Evaluation and Review Technique (PERT). For each activity, three estimates were considered: optimistic (a), most likely (m), and pessimistic (b), to reflect uncertainties such as university approvals, sponsor coordination, and event preparation.

The expected duration for each task was calculated using the PERT formula:

TE = (a + 4m + b) / 6

This approach ensures a realistic and flexible schedule while accounting for possible delays. Activities related to the actual event execution are considered deterministic, as they occur within a fixed timeframe (event day).

WBS Code	Activity Name	Description	Optimistic (a)	Most Likely (m)	Pessimistic (b)	Expected Time (TE)
1.1 Conceptualization (Project Initiation)						
1.1.1	Select event concept (A)	Select the University Sports Day Challenge concept and define objectives, scope, and purpose	0.5	1	2	1.1
1.1.2	Prepare	Prepare detailed	2	3	4	3.0

	proposal (B)	proposal including objectives, resources, and requirements				
1.1.3	Coordinate university (C)	Coordinate with departments for planning and approval process	0.5	1	1.5	1.0
1.1.4	Obtain approval (D)	Obtain official approval from university and DSA	1	2	3	2.0
1.1.5	Identify stakeholders (E)	Identify stakeholders including sponsors and participants	0.5	1	1.5	1.0
1.2 Planning & Preparation						
1.2.1	Meet university (F)	Meet university to confirm requirements and venue availability	6	11	16	11.0
1.2.2	Confirm sponsors (G)	Contact and confirm sponsors and support	5	10	15	10.0
1.2.3	Finalize format (H)	Finalize event structure, stations, and timeline	4	8	12	8.0
1.2.4	Plan activities (I)	Develop sports games and engagement activities	1	2	3	2.0
1.2.5	Assign roles (J)	Assign team roles and confirm timelines	13	19	25	19.0
1.2.6	Promote event (K)	Promote event via posters and social media	0.5	1	2	1.1
1.2.7	Secure	Arrange prizes and	2	3	4	3.0

	prizes (L)	giveaways for participants				
1.3 Event Execution						
1.3.1	Setup event (M)	Prepare venue and equipment	0.5	1	1.5	1.0
1.3.2	Run activities (N)	Execute sports activities	0.5	1	1.5	1.0
1.3.3	Monitor event (O)	Monitor flow and participant engagement	0.5	1	1.5	1.0
1.3.4	Distribute rewards (P)	Distribute prizes to winners	0.5	1	1.5	1.0
1.3.5	Record participation (Q)	Record attendance and participation	0.5	1	1.5	1.0
1.3.6	Manage operations (R)	Ensure smooth coordination and operations	0.5	1	1.5	1.0
1.4 Evaluation & Reporting						
1.4.1	Collect feedback (S)	Collect feedback via surveys	0.5	1	2	1.1
1.4.2	Analyze results (T)	Analyze participation and feedback	7	10	13	10.0
1.4.3	Prepare report (U)	Prepare final project report	1	2	3	2.0
1.4.4	Finalize report (V)	Finalize and submit report	2	3	4	3.0

Activity Name	Duration (Days)	Predecessor
1.1 Conceptualization (Project Initiation)		
1.1.1 Select event concept (A)	1.1	—
1.1.2 Prepare project proposal (B)	3.0	1.1.1
1.1.3 Coordinate with university (C)	1.0	1.1.2
1.1.4 Obtain approval (D)	2.0	1.1.3

1.1.5 Identify stakeholders (E)	1.0	1.1.1
1.2 Planning & Preparation		
1.2.1 Meet university & confirm requirements (F)	11.0	1.1.5
1.2.2 Confirm sponsors (G)	10.0	1.2.1
1.2.3 Finalize event format (H)	8.0	1.2.2
1.2.4 Plan games (I)	2.0	1.2.3
1.2.5 Assign roles (J)	19.0	1.1.4
1.2.6 Promote event (K)	1.1	1.2.5
1.2.7 Secure prizes (L)	3.0	1.2.2
1.3 Event Execution		
1.3.1 Setup event (M)	1.0	1.2.3, 1.2.4, 1.2.6, 1.2.7
1.3.2 Run activities (N)	1.0	1.3.1
1.3.3 Monitor competitions (O)	1.0	1.3.2
1.3.4 Distribute rewards (P)	1.0	1.3.3
1.3.5 Record participation (Q)	1.0	1.3.1
1.3.6 Manage operations (R)	1.0	1.3.1
1.4 Evaluation & Reporting		
1.4.1 Collect feedback (S)	1.1	1.3.1
1.4.2 Analyze results (T)	10.0	1.4.1
1.4.3 Prepare report (U)	2.0	1.4.2
1.4.4 Finalize report (V)	3.0	1.4.3

Justification for Project Schedule

The project schedule for the University Sports Day Challenge was developed using the PERT method to ensure realistic and reliable time estimates. By considering optimistic, most likely, and pessimistic scenarios, the team accounted for uncertainties related to approvals, sponsor coordination, and event preparation.

Activities were logically sequenced based on their dependencies to ensure a smooth workflow. Tasks such as approvals and planning phases were assigned longer durations due to their complexity and uncertainty, while execution activities were treated as fixed since they occur within a single event day.

Overall, this approach ensures that the schedule is structured, practical, and capable of handling potential delays while maintaining successful project completion.

Sign-off documentation

Approval and Sign-Off

The activity duration estimates and project schedule have been reviewed and approved by key stakeholders involved in the University Sports Day Challenge.

Project Sponsor: _____

Project Manager: _____

Team Members: _____

This sign-off confirms that the estimated durations and scheduling assumptions are realistic and aligned with project objectives.

3.2 Gantt Chart Overview

The Gantt chart provides a clear and structured visualization of the project timeline for the University Sports Day Challenge. It illustrates the start and end dates of each task, the overlap of activities, and the progression of the project from initial planning to final completion. The chart enhances coordination, planning efficiency, and time management by integrating both a detailed task table and a visual timeline. The total estimated project duration is 34 days, spanning from April 1, 2026 to May 4, 2026. No significant lag time was required, as activities were scheduled to ensure a continuous workflow.

3.2.1 Gantt Chart Table Overview


TASK ID	Task Description	Task Number	Predecessor	Resource	START DATE	WORK DAYS	END DATE	Critical Path
1.1.1	select topic	Task 01		Project Team	01-Apr-26	1	01-Apr-26	
1.1.2	prepare project proposal	Task 02	1	Project Team	02-Apr-26	3	06-Apr-26	YES
1.1.3	coordinate with university department	Task 03	2	Coordination Team	05-Apr-26	1	05-Apr-26	YES
1.1.4	obtain approval from administration (Milest	Task 04	3	Management	06-Apr-26	2	07-Apr-26	YES
1.1.5	identify key stakeholders	Task 05	1	Project Team	01-Apr-26	1	01-Apr-26	
1.2.1	meet with university department	Task 06	4	Coordination Team	02-Apr-26	10	15-Apr-26	YES
1.2.2	confirm sponsors	Task 07	6	Marketing Team	12-Apr-26	8	21-Apr-26	
1.2.3	finalize event format and presentation	Task 08	7	Planning Team	15-Apr-26	4	20-Apr-26	YES
1.2.4	plan activities and games (Planning Compl	Task 09	8	Planning Team	17-Apr-26	2	20-Apr-26	YES
1.2.5	assign roles and responsibilities	Task 10	4	Project Team	06-Apr-26	12	21-Apr-26	YES
1.2.6	promote event (flyers/social media)	Task 11	10	Marketing Team	18-Apr-26	2	20-Apr-26	
1.2.7	prepare prizes and materials	Task 12	8	Logistics Team	15-Apr-26	3	17-Apr-26	
1.3.1	event execution (Event Day)	Task 13	12	Operations Team	20-Apr-26	1	20-Apr-26	YES
1.3.2	event execution (Event Day)	Task 14	13	Operations Team	20-Apr-26	1	20-Apr-26	YES
1.3.3	event execution (Event Day)	Task 15	14	Operations Team	20-Apr-26	1	20-Apr-26	YES
1.3.4	event execution (Event Day)	Task 16	15	Operations Team	20-Apr-26	1	20-Apr-26	YES
1.3.5	event execution (Event Day)	Task 17	16	Operations Team	20-Apr-26	1	20-Apr-26	YES
1.3.6	event execution (Event Day)	Task 18	17	Operations Team	20-Apr-26	1	20-Apr-26	YES
1.4.1	collect feedback	Task 19	18	Project Team	21-Apr-26	1	21-Apr-26	
1.4.2	analyze results	Task 20	19	Analysis Team	22-Apr-26	7	30-Apr-26	YES
1.4.3	prepare final report	Task 21	20	Project Manager	29-Apr-26	2	30-Apr-26	YES
1.4.4	finalize report	Task 22	21		01-May-26	3	05-May-26	

The Gantt chart table presents a structured breakdown of all project activities based on the Work Breakdown Structure (WBS), including task descriptions, start dates, end dates, and durations. This table forms the foundation of the project schedule by organizing tasks in a logical and sequential manner.

Initial tasks such as topic selection, proposal preparation, coordination with the university, and approval processes are completed early in the timeline, establishing the foundation of the project. The planning phase includes overlapping activities such as sponsor confirmation, role assignment, and event preparation, reflecting efficient time management and coordination.

The event execution phase is concentrated on a single day, April 20, 2026, where all operational activities such as setup, activity execution, monitoring, and reward distribution occur simultaneously. The final phase consists of evaluation and reporting tasks, including feedback collection, analysis, and report preparation, marking the completion of the project. Additionally, material preparation and prize arrangements were scheduled prior to the event day to ensure timely availability of required resources

3.2.2 Gantt Chart Graph Overview

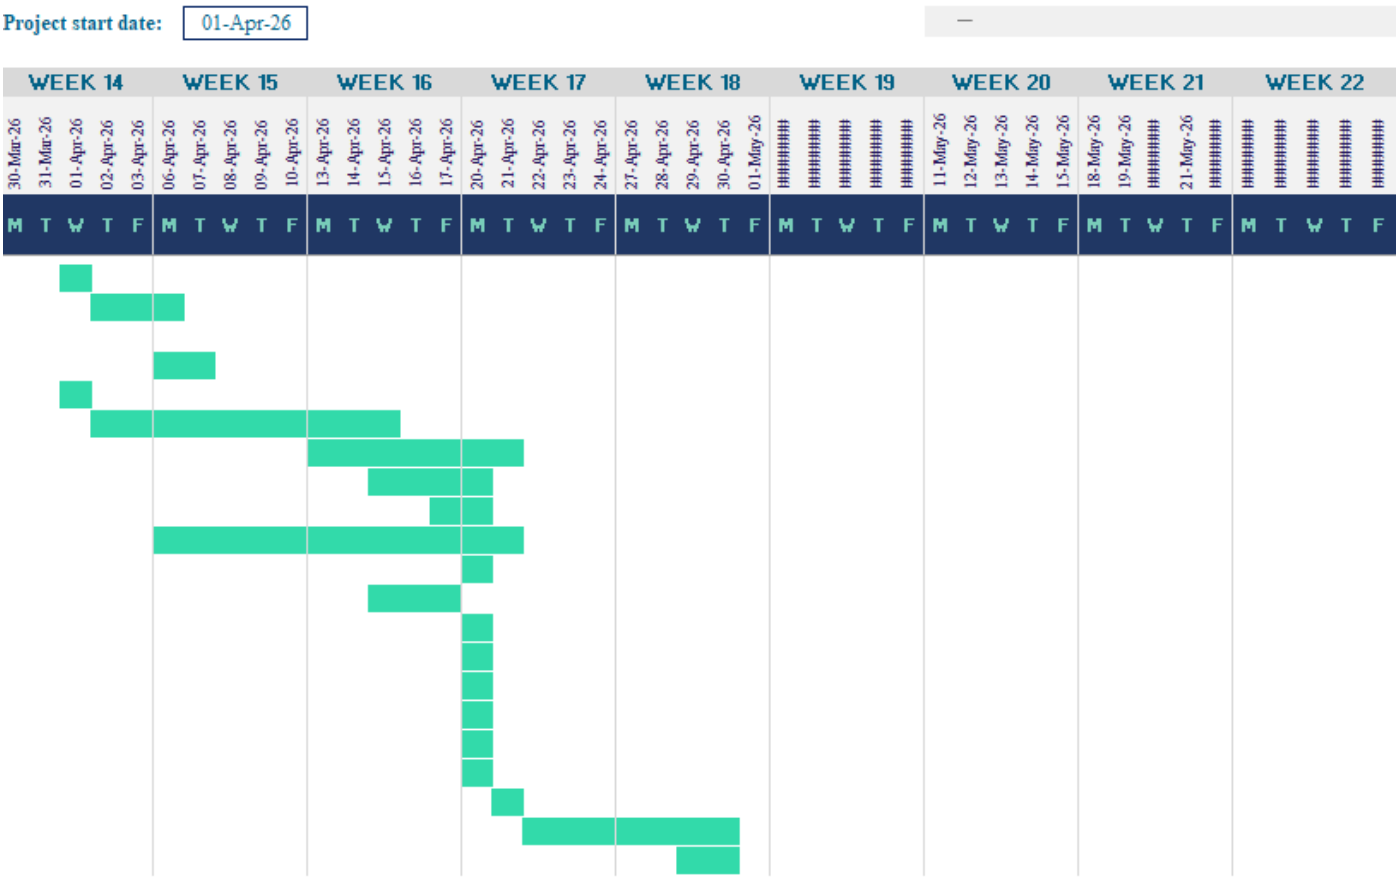

The Gantt chart graph visually represents the project schedule by illustrating each task as a horizontal bar according to its designated start and finish dates. The vertical axis lists the tasks based on their sequence in the Work Breakdown Structure, while the horizontal axis represents the project timeline in calendar dates.


At the beginning of the timeline, short-duration bars represent initial conceptualization tasks such as topic selection and stakeholder identification. As the project progresses, longer and overlapping bars appear during the planning phase, indicating simultaneous execution of multiple activities such as coordination, sponsorship confirmation, and role assignment.

A key visual feature of the chart is the clustering of tasks on April 20, 2026, which represents the event execution day. Multiple activities occur concurrently, highlighting the coordination required during the event. Following the event, the chart transitions into the evaluation phase, where tasks such as data analysis and report preparation extend beyond the event day.

Overall, the Gantt chart clearly demonstrates task sequencing, overlapping activities, and workload distribution, ensuring effective project planning and timely completion.

3.3 Activity Network

3.3.1 Activity-on-Node (AON) Network Diagram

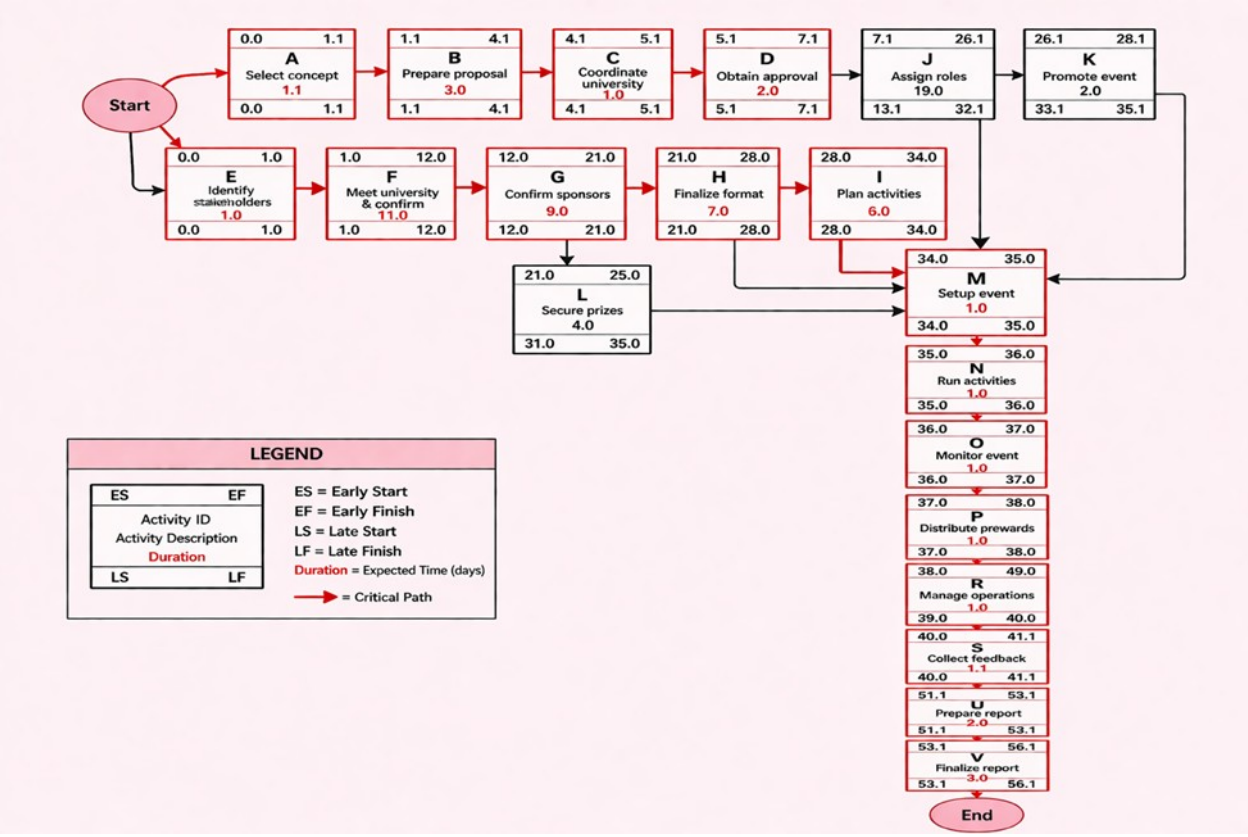

Justification for the Project Network Diagram

We developed a visual representation of the University Sports Day Challenge using an Activity-on-Node (AON) network diagram in order to clearly illustrate the logical sequencing of project activities and the overall timeline. The diagram provides a structured view of how tasks are interconnected, from initial planning stages through event execution and final project closure.

1. Task Dependencies

The network diagram clearly identifies the dependencies between activities. Specifically:

- Activity M (Setup event venue) cannot begin until multiple preceding activities are completed, including Activities I (Plan activities), K (Promote event), and L (Prepare prizes and materials). This represents a key merge point where several parallel paths converge before the execution phase begins.
- Activities in the planning phase, such as stakeholder identification (Activity E) and proposal preparation (Activity B), occur concurrently after the initial concept selection (Activity A), demonstrating parallel task execution to improve efficiency.

- Activity D (Obtain approval from administration) is a critical dependency that must be completed before major planning activities such as assigning roles (Activity J) and further coordination can proceed.

The diagram effectively highlights both sequential and parallel relationships, ensuring clarity in task execution order.

2. Correctly Managing the Schedule

Following the estimation of activity durations using the PERT method, the AON network was used to calculate key scheduling parameters:

- Early Start (ES) and Early Finish (EF), which represent the earliest possible times each activity can begin and end.
- Late Start (LS) and Late Finish (LF), which indicate the latest times activities can occur without delaying the overall project.
- Float (Slack), which measures the flexibility available for non-critical activities without affecting the final completion date.

These calculations enable effective scheduling control and allow for better monitoring of project progress.

3. Identification of the Critical Path

The longest continuous sequence of dependent activities has been identified as the critical path of the project:

(A → B → C → D → F → G → H → I → M → N → O → P → R → S → T → U → V)

This path represents the minimum time required to complete the project. Any delay in activities along this path will directly impact the overall project completion date. Therefore, these activities require close monitoring and strict time management to ensure the project remains on schedule.

4. Resource Maximization

The presence of parallel paths within the network, such as early planning tasks and stakeholder-related activities, allows for efficient allocation of resources. By executing independent activities simultaneously, the project team can reduce idle time and optimize productivity. Additionally, the network highlights areas where tasks may be compressed or reallocated if necessary to meet deadlines.

5. Risk Management

The AON network serves as an effective tool for identifying potential risks within the project schedule. Key risk indicators include:

- Merge points, such as Activity M, where delays in any preceding task can affect the start of the event execution phase.
- Activities on the critical path, which have zero float and therefore no scheduling flexibility.
- Opportunities to utilize float in non-critical activities to mitigate delays without impacting the overall project timeline.

By identifying these elements, project managers can proactively manage risks and maintain control over project execution.

4. Project Budget

This section includes activity cost estimation and the project budget for the Sports Day Challenge Event. All direct and indirect costs, resource requirements, cost estimation methods, and time-phased budgeting are presented in this section. Building on Assignments 1, 2, and 3, this section converts the approved project plan into a realistic financial plan to ensure successful project execution within available student resources.

The project was organized and managed by a four-member student project management team and supported by university stakeholders, volunteers, and university facilities. Since several resources were provided by Effat University, the team was able to control costs and focus spending on prizes, materials, and event execution.

4.1 Project Resources

This part highlights all human resources required for the Sports Day Challenge Event and prepares a fully loaded cost table based on applying cost management principles from Chapters 8 and 12. The section includes both the theoretical economic value of project resources and the actual project execution model, where many resources were provided voluntarily or through university support.

The Sports Day Challenge was planned and executed by a student project management team, with additional support from university administration, volunteers, and university sports facilities. Because the event relied heavily on internal support and volunteerism, the actual financial burden was significantly lower than the theoretical resource value.

Resource / Role	Organization	Employment Status	Exemption Status
Project Coordinator (Talah)	Effat University	Part-Time (Student)	Non-Exempt

Resource / Role	Organization	Employment Status	Exemption Status
Operations Lead (Youssef)	Effat University	Part-Time (Student)	Non-Exempt
Sponsorship & External Relations Lead (Sara)	Effat University	Part-Time (Student)	Non-Exempt
Marketing & Registration Lead (Taleen)	Effat University	Part-Time (Student)	Non-Exempt
Course Instructor (Dr. Sarah Osailan)	Effat University	Full-Time (Faculty)	Exempt
Dean of College of Business (Dr. Sara Alzarka)	Effat University	Full-Time (Faculty)	Exempt
Dean of Student Affairs (Dr. Pakenam Shiha)	Effat University	Full-Time (Staff)	Exempt
Sports Activities Supervisor (Dr. Tamer)	Effat University	Full-Time (Staff)	Exempt
Student Volunteers (24 Volunteers)	Effat University	Part-Time / Volunteer	Non-Exempt
DJ / Music Volunteer	Effat University	Part-Time / Volunteer	Non-Exempt
Door Access Volunteer (Girls Session)	Effat University	Part-Time / Volunteer	Non-Exempt

Non-Human Project Resources

Resource	Source	Cost Status
Basketball Court	Effat University	Provided Free
Dumbbells	Effat University	Provided Free
Yoga Mats	Effat University	Provided Free
Cones / Timer	Effat University	Provided Free
Posters	Purchased by Team	Paid
Team Shirts	Purchased by Team	Paid

Method for Developing Fully Loaded Costs

To satisfy project budgeting requirements from Chapters 8 and 12, two costing views were used:

1. Theoretical Costing Approach: estimates the economic value of student labor, university staff support, volunteers, and facilities if charged commercially.
2. Actual Costing Approach: reflects the real event cost, where labor was voluntary and facilities were provided by Effat University.

Formula:

Fully Loaded Cost = (Hourly Rate × Hours Worked) + Overhead Allowance

Assumptions:

- Student Team Rate: SAR 35/hour
- University Staff Equivalent: SAR 220/hour
- Volunteer Labor: No actual charge
- Overhead Factor: 15%

Fully Loaded Resource Cost Table

Personnel / Job Title	Hourly Rate (SAR)	Hours Needed	Direct Labor Cost (SAR)	Overhead Charge	Cost with Overhead (SAR)	Personal Time	Fully Loaded Cost (SAR)
Project Coordinator (Talah)	35	22	770	1.15	886	1.10	975
Operations Lead (Youssef)	35	24	840	1.15	966	1.10	1,063
Sponsorship & External Relations Lead (Sara)	35	18	630	1.15	725	1.10	798
Marketing, Registration & Volunteer Lead (Taleen)	35	20	700	1.15	805	1.10	886
Course Instructor (Dr. Sarah Osailan)	220	5	1,100	1.15	1,265	1.10	1,392
Dean of College of Business (Dr. Sara Alzarka)	220	3	660	1.15	759	1.10	835
Dean of Student Affairs (Dr. Pakenam Shiha)	220	4	880	1.15	1,012	1.10	1,113
Sports Supervisor (Dr. Tamer)	180	5	900	1.15	1,035	1.10	1,139
Student Volunteers (24 volunteers)	20	48	960	1.15	1,1		

Where We Found the Numbers

1. Hours Required (152 total hours)

- Estimated based on the Assignment 3 project schedule and actual event activities, including:
- Planning meetings and coordination
- Sponsor communication attempts
- Registration management
- Volunteer scheduling
- Poster design and printing preparation
- Venue setup and equipment arrangement

- Event execution and supervision
- Score calculation and prize distribution
- Project close-out activities

2. Hourly Rates

- Hourly rates were estimated using realistic equivalent values for student event management roles, university staff support, and volunteer contributions. These rates were used for academic budgeting purposes only.

3. Cost Multipliers

- Standard cost management principles were applied:
- Overhead Charge = administrative support, communication, utilities, and coordination costs
- Personal Time Multiplier = additional effort beyond scheduled working hours

Justification

This method demonstrates the theoretical economic value of all resources used in the Sports Day Challenge Event. Although many individuals contributed voluntarily, the project still required significant labor hours, planning effort, supervision, and institutional support. If the same event had been fully outsourced commercially, the total resource value would have exceeded SAR 9,500.

Actual Project Costs (Real-World Execution)

The following table presents the actual resource cost structure of the Sports Day Challenge Event. Unlike the theoretical fully loaded model, the event was implemented through volunteer labor, shared student effort, and free institutional support provided by Effat University. Therefore, no labor charges or overhead expenses were directly incurred.

Total Project Cost = Direct Material Costs + Contingency Reserve

Personnel / Job Title	Hourly Rate	Hours Needed	Direct Cost	Overhead	Cost with Overhead	Personal Time	Fully Loaded Cost
Student Volunteers (24 volunteers)	20	48	960	1.15	1,104	1.10	1,214
DJ Volunteer	25	2	50	1.15	58	1.10	64
Door Access Volunteer	20	1	20	1.15	23	1.10	25
PROJECT GRAND TOTAL		152	7,510				9,504

Actual Cost Analysis Summary

- Total Direct Labor Cost: SAR 0
- Total Indirect Costs: SAR 0
- Total Fully Loaded Labor Cost: SAR 0
- Material, Printing & Prize Costs: SAR 1,200
- Total Actual Project Cost: SAR 1,200

Justification

This analysis shows that the Sports Day Challenge Event was successfully executed through effective use of volunteer resources, university institutional support, and shared financial contributions from project team members. While the actual cash expenditure was limited to SAR 1,200, the estimated economic value of the event resources exceeded SAR 9,500. This reflects strong resource utilization, teamwork, and cost-efficient project execution.

4.2 Other Costs

This section identifies all significant non-labor costs associated with the Sports Day Challenge Event. These costs include direct material purchases, prizes, printing, event setup items, operational supplies, contingency reserve, and indirect in-kind support received from Effat University and volunteers. The project team minimized spending by relying on university resources and shared team contributions.

Cost Breakdown by Category

Cost Category	Item Description	Quantity	Total Cost (SAR)	Cost Type
Winner Rewards	First Place Cash Prizes	1 package	700	Direct
Third Place Rewards	Protein bars / chips / shakes	Assorted	100	Direct
Printing	Posters & challenge instructions	Multiple	100	Direct
Team Setup	Colored shirts / markers	Set	80	Direct
Operations Supplies	Water, tape, pens, misc. items	Lump Sum	70	Direct
Contingency Reserve	Unexpected expenses	Lump Sum	150	Indirect
Grand Total Project Cost			**1,200 SAR**	

Indirect / Sponsored / In-Kind Costs

Item	Cost Impact	Classification
Basketball Court Venue	Provided free by university	Indirect Support
Mats / Dumbbells / Equipment	Provided free by university	Indirect Support
Volunteer Labor	No direct charge	In-Kind Contribution

Item	Cost Impact	Classification
PT Sessions for 2nd Place Winners	Free contribution by Youssef	Sponsored Prize
Administrative Support / Approvals	No direct charge	Indirect Support

Cost Classification Summary

Direct Costs

Costs that were directly traceable to event execution, such as prizes, printing, shirts, and operational supplies.

Indirect Costs

Costs not directly charged to the team but necessary for project success, including venue access, equipment support, and administrative approvals.

Fixed Costs

Costs that remained unchanged regardless of attendance numbers, such as poster printing and first-place prizes.

Variable Costs

Costs that could change depending on participation levels, such as refreshments, giveaway items, or contingency usage.

Expediting Costs

No expediting costs were incurred, as the project was completed according to schedule without rush purchases or emergency outsourcing.

Justification

The Sports Day Challenge Event was completed using a modest and controlled student budget of **SAR 1,200**. Most spending focused on participant motivation, event communication materials, and operational readiness. Significant cost savings were achieved through the use of free university facilities, volunteer labor, and donated second-place prizes. This demonstrates effective project cost control and efficient resource utilization.

4.3 Cost Estimates

This section presents the cost estimation process used for the Sports Day Challenge Event. Ballpark, comparative, feasibility, and definitive estimates were developed progressively as more project information became available. As the project moved from planning to execution, the level of estimate accuracy improved. This section also identifies the participants involved in the cost estimate exercise, the information gathered to support the estimates, and the final approved project budget.

Participants in the Cost Estimate Exercise

The cost estimates were developed collaboratively by the student project management team based on each member's area of responsibility.

Name	Contribution
Talah	Coordinated total budget, approvals, and final review
Youssef	Provided operational cost estimates and prize planning
Sara	Reviewed sponsorship opportunities and external support
Taleen	Estimated registration, printing, and volunteer-related needs
Entire Team	Reviewed and approved final budget

Information Gathered to Support Estimates

- The project team collected the following information before finalizing the cost estimates:
- Expected number of competing teams: 12 teams (24 competitors)
- Estimated audience attendance: approximately 100 students
- Number of volunteers required: 24 volunteers
- Prize expectations to encourage student participation
- Printing requirements for posters and challenge instructions
- Availability of free university venue and sports equipment
- Team identification materials such as shirts and markers
- Operational supply needs including water, tape, and pens
- Previous costs observed in similar university student events
- Available financial contributions from team members

4.3.1 Ballpark Estimate (Week 1)

The ballpark estimate was prepared during the early planning stage before detailed requirements were finalized. It was based on rough expected spending ranges.

Cost Component	Estimated Range (SAR)
Materials & Printing	150 – 400
Prizes	700 – 1,000
Miscellaneous	100 – 250
Total Ballpark Estimate	**950 – 1,650**

Estimated Accuracy: ±30%

4.3.2 Comparative Estimate (Week 2)

The comparative estimate was based on reviewing similar student activities and small competitions previously organized at the university.

Cost Driver	Comparative Estimate (SAR)
Student Competition Rewards	800
Printing / Promotion	150
Event Supplies	100
Contingency	150
Total Comparative Estimate	**1,200**

Estimated Accuracy: ±15%

4.3.3 Feasibility Estimate (Week 3)

The feasibility estimate was prepared after confirming that the university would provide the venue, equipment, and volunteer support at no direct cost.

Cost Category	Amount (SAR)
Direct Materials	350
Rewards	800
Reserve	50
Total Feasibility Estimate	**1,200**

Estimated Accuracy: ±10%

4.3.4 Definitive Final Estimateand Project Budget

The definitive estimate was prepared after planning activities were completed and final project requirements were confirmed.

Cost Category	Final Amount (SAR)
Prizes & Rewards	800
Printing & Promotion	100
Team Setup Materials	80
Miscellaneous Supplies	70
Contingency Reserve	150
Final Approved Budget	**1,200 SAR**

Estimated Accuracy: ±5%

4.3.5 Budget Accuracy Improvement

Estimation Phase	Total Estimate	Accuracy
Ballpark	950 – 1,650	±30%
Comparative	1,200	±15%
Feasibility	1,200	±10%
Definitive	1,200	±5%

This progression shows that estimate accuracy improved as additional project information became available and planning uncertainty was reduced.

Final Budget Sign-Off

The final project budget of **SAR 1,200** was reviewed and approved by the relevant project stakeholders.

Stakeholder	Role	Approval Status
Student Project Management Team	Internal Budget Approval	Approved
Dr. Sarah Osailan	Course Instructor	Approved
Dr. Pakenam Shiha	Dean of Student Affairs	Approved
Dr. Sara Alzarka	Dean, College of Business	Approved

Justification

The final budget reflects a realistic and cost-efficient student event plan. Most direct spending was allocated to participant rewards, communication materials, and operational readiness, while significant savings were achieved through university support, volunteer labor, and internal contributions from the project team. This demonstrates effective cost planning and responsible budget management.

4.4 Time-Phased Budget

This section presents the distribution of the Sports Day Challenge Event budget across the project timeline. A **weekly time-phased budgeting approach** was used to monitor spending and ensure cost control at each stage of the project lifecycle.

The allocation of costs was based on the **type of activities performed each week**, ensuring that resources were used efficiently and aligned with project needs.

TIME-PHASED BUDGET TABLE

Week	Main Activity	Estimated Cost (SAR)	Cost Explanation
Week 1	Initial planning, approvals, team coordination	50	Minimal costs due to internal meetings and university support

Week 2	Promotion, registration, poster printing	150	Costs driven by printing materials and awareness campaigns
Week 3	Purchasing prizes, shirts, and supplies	350	Medium cost phase due to procurement of rewards and materials
Week 4	Event execution (main event day)	600	Highest cost phase including prizes, refreshments, and operations
Week 5	Project close-out and contingency	50	Final adjustments and unused contingency allocation

Total Project Budget: SAR 1,200

Budget Distribution Analysis

The time-phased budget shows that **costs increased gradually throughout the project**, with the highest spending occurring during **Week 4**, which represents the event execution phase.

Early stages (Weeks 1–2) required **low financial investment**, focusing mainly on planning and promotion. Mid-stage (Week 3) involved **resource preparation**, while the final stage required **maximum spending** to deliver the event successfully.

This structure reflects a **typical project cost curve**, where expenditures peak during execution and decrease during project close-out.

Justification

This budgeting approach allowed the team to:

- Monitor spending **week by week**
- Align costs with **project activities**
- Ensure the project stayed **within the approved budget**

Overall, the time-phased budget supported effective cost control and contributed to the successful execution of the Sports Day Challenge Event.

4.4.1 Weekly Budget Allocation

Week	Main Activity	Estimated Cost (SAR)
Week 1	Initial planning meetings, approvals, and coordination	50
Week 2	Registration, promotion, posters, and announcements	150
Week 3	Purchase prizes, shirts, and operational supplies	350
Week 4	Event execution day costs, winner rewards, refreshments	600
Week 5	Project close-out and contingency use	50
Total Project Budget		1,200 SAR

4.4.2 Budget Distribution Analysis

The largest portion of the budget was allocated to Week 4, as this phase included the actual event day, winner rewards, refreshments, and final operational needs. Lower costs were incurred during the planning and close-out stages, while mid-project costs focused on promotion and purchasing required materials.

Stakeholder Sign-Off

We, the undersigned, reviewed and approved the final project budget of SAR 1,200 for the Sports Day Challenge Event.

Stakeholder	Title	Status
Dr. Pakenam Shiha	Dean of Student Affairs	Approved
Dr. Sarah Osailan	Course Instructor	Approved
Dr. Sara Alzarka	Dean, College of Business	Approved
Student Project Management Team	Internal Approval	Approved

Budget Summary

The Sports Day Challenge Event was successfully planned and executed using a realistic student budget of **SAR 1,200**. The event supported **12 competing teams (24 competitors)**, approximately **100 attendees**, and **24 volunteers**. Through effective cost control, volunteer contribution, university support, and shared project management responsibilities, the team delivered a successful campus event while remaining within budget.

5. Project Close-Out

This section presents all necessary project close-out documentation for the Sports Day Challenge Event. It includes confirmation of completed work, financial closure, lessons learned, and formal stakeholder sign-

off. The close-out ensures that all project activities were completed according to the approved scope, budget, and schedule, and that all outcomes are properly documented.

5.1 Close Cost Accounts

All project financial activities have been reviewed and formally closed.

- **Final Approved Budget:** SAR 1,200
- **Actual Project Cost:** SAR 1,200
- **Budget Variance:** SAR 0

All expenses were aligned with the approved budget categories, including:

- Prizes and rewards
- Printing and promotion
- Team setup materials
- Operational supplies
- Contingency reserve

No outstanding payments, debts, or financial obligations remain. Since labor and facilities were provided voluntarily or by the university, no additional financial closeout actions were required.

5.2 Lessons Learned

A Lessons Learned assessment was conducted to evaluate project performance, identify challenges, and improve future events.

What Went Well:

- Strong teamwork and clear role distribution among project members
- Effective use of volunteer resources
- Successful cost control and staying within budget
- High participant engagement and smooth event flow
- Efficient use of university facilities and equipment

Challenges Faced:

- Limited participant registration in early stages
- Last-minute coordination pressure before event day

- Dependence on volunteers required close supervision
- Minor delays in station transitions during peak time

Mitigation Strategies Used:

- Increased promotional efforts to attract participants
- Real-time coordination and communication among team members
- Flexible adjustments to event flow during execution
- Assigning clear responsibilities to volunteers

Suggestions for Future Projects:

- Start promotion earlier to secure higher participation
- Use digital registration tracking tools for better organization
- Allocate buffer time between activity stations
- Increase contingency budget slightly for flexibility
- Assign a dedicated on-site coordinator for real-time control

5.3 Work Completion & Documentation

The Sports Day Challenge Event was successfully completed on the scheduled date. All planned activities were executed as defined in the project scope and schedule. The following key deliverables were completed:

- Organization of 12 competing teams (24 participants)
- Execution of all challenge stations (basketball, push-ups, planks, etc.)
- Volunteer coordination and station management
- Score tracking and fair evaluation process
- Prize distribution for winners (1st, 2nd, and 3rd place)
- Event supervision and safety management

All event materials, including registration records, participant tracking sheets, volunteer lists, and scoring sheets, were documented and stored for reference.

No major configuration changes were required during execution. Minor adjustments (such as timing flow between teams) were handled on-site without impacting overall project success.

5.3 Supplier & Support Closure

Although the project did not rely on external commercial suppliers, all support contributions were completed and acknowledged:

- University facilities (basketball court, equipment) were used and returned in proper condition
- Volunteer roles were completed successfully with no pending responsibilities
- Sponsored contributions (e.g., personal training sessions for second-place winners) were delivered as promised

All support services were completed without disputes, delays, or quality issues

5.4 Client / Stakeholder Sign-Off

The project outcomes were reviewed and accepted by all relevant stakeholders. The event met its objectives of promoting physical activity, student engagement, and a healthy lifestyle.

Stakeholder satisfaction was confirmed through:

- Positive participant feedback
- Successful event execution without major issues
- Achievement of planned participation and attendance targets

Formal approval and acceptance were provided by:

- Course Instructor (Dr. Sarah Osailan)
- Dean of Student Affairs (Dr. Pakenam Shiha)
- Dean of College of Business (Dr. Sara Alzarka)
- Student Project Management Team

5.6 Action Plan for Future Projects

Based on lessons learned, the following action plan is recommended:

- Improve early-stage planning and marketing timeline
- Enhance volunteer training and briefing before event day
- Standardize event templates (registration, scoring, schedules)
- Develop a clearer risk management plan
- Strengthen communication channels during execution

5.7 Final Project Evaluation

The Sports Day Challenge Event is considered **successful** based on:

- Completion within scope, time, and budget
- Positive stakeholder and participant feedback
- Effective teamwork and coordination
- Strong cost efficiency (low actual cost vs. high resource value)

The project demonstrated practical application of project management principles, including planning, budgeting, execution, and control.

